

# ACCELERATED DISTRIBUTION DEMONSTRATION SYSTEM

## REGULATORY INFORMATION DISTRIBUTION SYSTEM (RIDS)

ACCESSION NBR: 9009180004    DOC. DATE: 90/09/07    NOTARIZED: NO    DOCKET #  
 FACIL: 50-250 Turkey Point Plant, Unit 3, Florida Power and Light C    05000250  
 50-251 Turkey Point Plant, Unit 4, Florida Power and Light C    05000251

AUTH. NAME                      AUTHOR AFFILIATION  
 HARRIS, K.N.                    Florida Power & Light Co.  
 RECIP. NAME                    RECIPIENT AFFILIATION  
                                   Document Control Branch (Document Control Desk)

SUBJECT: Forwards Jul 1990 integrated schedule regulatory rept for facilities.

DISTRIBUTION CODE: A001D    COPIES RECEIVED: LTR 1 ENCL 1    SIZE: 20  
 TITLE: OR Submittal: General Distribution

NOTES:

	RECIPIENT		COPIES			RECIPIENT		COPIES	
	ID CODE/NAME	LTR	ENCL	ID CODE/NAME		LTR	ENCL		
	PD2-2 LA	1	1	PD2-2 PD	1	1			
	EDISON, G	2	2						
INTERNAL:	NRR/DET/ECMB 9H	1	1	NRR/DOEA/OTSB11	1	1			
	NRR/DST 8E2	1	1	NRR/DST/SELB 8D	1	1			
	NRR/DST/SICB 7E	1	1	NRR/DST/SRXB 8E	1	1			
	NUDOCS-ABSTRACT	1	1	OC/LFMB	1	0			
	OGC/HDS2	1	0	<u>REG FILE 01</u>	1	1			
	RES/DSIR/EIB	1	1						
EXTERNAL:	NRC PDR	1	1	NSIC	1	1			

NOTE TO ALL "RIDS" RECIPIENTS:

PLEASE HELP US TO REDUCE WASTE! CONTACT THE DOCUMENT CONTROL DESK, ROOM P1-37 (EXT. 20079) TO ELIMINATE YOUR NAME FROM DISTRIBUTION LISTS FOR DOCUMENTS YOU DON'T NEED!

TOTAL NUMBER OF COPIES REQUIRED: LTR 17 ENCL 15

*MA 4  
ub*

R  
I  
D  
S  
/  
A  
D  
D  
S  
  
R  
I  
D  
S  
/  
A  
D  
D  
S



SEP 07 1990

L-90-325

U. S. Nuclear Regulatory Commission  
Attn: Document Control Desk  
Washington, D. C. 20555


Gentlemen:

Re: Turkey Point Unit 3 and 4  
Docket No. 50-250 and 50-251  
Integrated Schedule Regulatory Report

Attached is the July, 1990, Integrated Schedule (I/S) Regulatory Report for the Turkey Point Plant. The schedules discussed in this report reflect information updated since the May, 1990, Regulatory Report which was submitted to the NRC on July 19, 1990. The changes to the schedules discussed in this report have been reviewed with the NRC Project Manager for the Turkey Point Plant in accordance with the Integrated Schedule Plan.

Should you have any questions regarding this report, please contact us.

Very truly yours,

  
K. N. Harris  
Vice President  
Turkey Point Plant Nuclear

KNH/DRP/DPS/ds

attachment

cc: Stewart D. Ebnetter, Regional Administrator, Region II, USNRC  
Senior Resident Inspector, USNRC, Turkey Point Plant

9009180004 900907  
PDR ADOCK 05000250  
R PDC

*Foot 111*

00033

ATTACHMENT 1

TURKEY POINT UNITS 3 AND 4

JULY, 1990 INTEGRATED SCHEDULE

The following is a summary of the I/S modifications for the Integrated Schedule Regulatory Report.

The July, 1990, Integrated Schedule is based on the following outages:

<u>OUTAGE DESCRIPTION</u>	<u>START</u>	<u>FINISH</u>
Unit 3 Diesel Tie-in	12/09/90	10/06/91
Unit 3 Cycle 13 Refueling	08/21/92	12/04/92
Unit 3 Cycle 14 Refueling	04/01/94	06/03/94
Unit 4 Cycle 13 Refueling	11/15/90	10/27/91
Unit 4 Cycle 14 Refueling	04/01/93	06/03/93
Unit 4 Cycle 15 Refueling	10/01/94	12/03/94

NRC COMMITTED MODIFICATIONS ADDED

<u>I/S #</u>	<u>UNIT - DESCRIPTION</u>	<u>LIC</u> <u>CAT</u>
- - - -	NONE - - - -	

NRC COMMITTED MODIFICATIONS COMPLETED

<u>I/S #</u>	<u>UNIT - DESCRIPTION</u>	<u>LIC</u> <u>CAT</u>
- - - -	NONE - - - -	

NRC COMMITTED MODIFICATIONS CANCELLED

<u>I/S #</u>	<u>UNIT - DESCRIPTION</u>	<u>LIC</u> <u>CAT</u>
- - - -	NONE - - - -	



11  
12  
13  
14  
15


16  
17

18  
19

20




NRC MODIFICATIONS WITH FORECAST COMPLETION DATES BEYOND THEIR COMMITTED DATES

<u>I/S #</u>	<u>UNIT - DESCRIPTION</u>	<u>LIC CAT</u>	<u>JUNE 1990</u>	<u>JULY 1990</u>	<u>NRC DATE JULY 1990</u>
550	3 NORMAL CTMT CLRS CTRL SWs	NRR	08/26/92	08/26/92	10/06/91
569	4 NORMAL CTMT CLRS CTRL SWs	NRR	04/06/93	04/06/93	10/27/91
792	S CTRL RM LIGHTING EVAL	NRR	07/26/90	09/13/90	07/01/90
1186	C SEC PLT ENTRANCE FACILITY	NRR	07/30/90	09/14/90	08/31/90
1246	4 TURB RUNBACK SLCTR SW REPL	NRR	04/01/93	04/01/93	10/27/91
1293	3 CTR LD METERS-ADD UNITS	NRR	09/24/92	09/24/92	10/06/91
1294	4 CTR LD METERS-ADD UNITS	NRR	05/05/93	05/05/93	10/27/91
1297	3 NIS-ELIM UNUSED SW POSITNS	NRR	09/24/92	09/24/92	10/06/91
1298	4 NIS-ELIM UNUSED SW POSITNS	NRR	05/05/93	05/05/93	10/27/91
787	C INSTL BARRIERS HVAC DUCTS	I&E	07/17/90	08/03/90	05/19/90
860	3 INST CTMT PHYS BARR/PREV	I&E	10/29/92	10/29/92	05/19/90
861	4 INST CTMT PHYS BARR/PREV	I&E	04/14/93	04/14/93	10/27/91
1313	3 SMALL BORE PIPING/NCR DISP	I&E	02/11/93	02/11/93	10/06/91



PROJECT ALMEGA99 CFO	TURKEY POINT NUCLEAR PLANT INTEGRATED SCHEDULE FLORIDA POWER AND LIGHT CO.	MODE TIFY INTERVAL - 1 YEAR(S)	TARGET SCHEDULE 20 TARG FINISH 17MAY95 TARG DATA DATE 29NOV88	RLN 2ALC90 18-53 PROJECT#2 8683 SCHEDULE BAR CHART
PAGE 1 SHEET 1	T A R G E T S C H E D U L E	SORT BREAKS BCODES 9 CUR EF		
START 23JAN84 FINISH 16AUG95 DATA DATE 28JUN90	LINE BREAK ON NRC COMMITMENT CATEGORIES LINE BREAK ON CFO SUB-SYSTEM			

				1989	1990	1991	1992	1993
CFO	POST TMI CONFIRMATORY MODIFICAT'N	C AREA RADIATION MONIT'G SYST REPL CFO MOD 0341	..... 18AUG89			31DEC90		
	P04-T11.20 U4 SEL SYS MODS/REPAIRS	C EDG AIR START MOTORS UPGRADE CFO MOD 0576	18JUL86			27OCT91	17APR91	
	POST PEP	4 RHR-INSTL UPGRADED 8" GLOBE VLV CFO MOD 0565	5FEB88			26NOV90	27OCT91	

NOTES:   
 ORIGINAL NRC COMMITMENT DATE  
 CURRENT NON-OUTAGE NRC COMMITMENT DATE  
 CURRENT OUTAGE NRC COMMITMENT DATE

DATA  
DATE



10-11-54


10-11-54


10-11-54

10-11-54




PROJECT ALHCA99	TURKEY POINT NUCLEAR PLANT	MODE TIFT	TARGET SCHEDULE	30	REV	2ALIC90	18 : 54
PIOT REG	INTEGRATED SCHEDULE	INTERVAL	TARG FINISH	17MAY95	PROJECT/2	8683	
PAGE 1 SHEET 1	FLORIDA POWER AND LIGHT CO.	1 YEAR(S)	TARG DATA DATE	29NOV88	SCHEDULE BAR CHART		
START 22JAN84	T A R G E T S C H E D U L E	SHORT BREAKS	CUR EF				
FINISH 16AUG95	PAGE BREAK VALUE: 2 - REG						
DATA DATE 28JUN 90	LINE BREAK ON NRC COMMITMENT CATEGORIES						

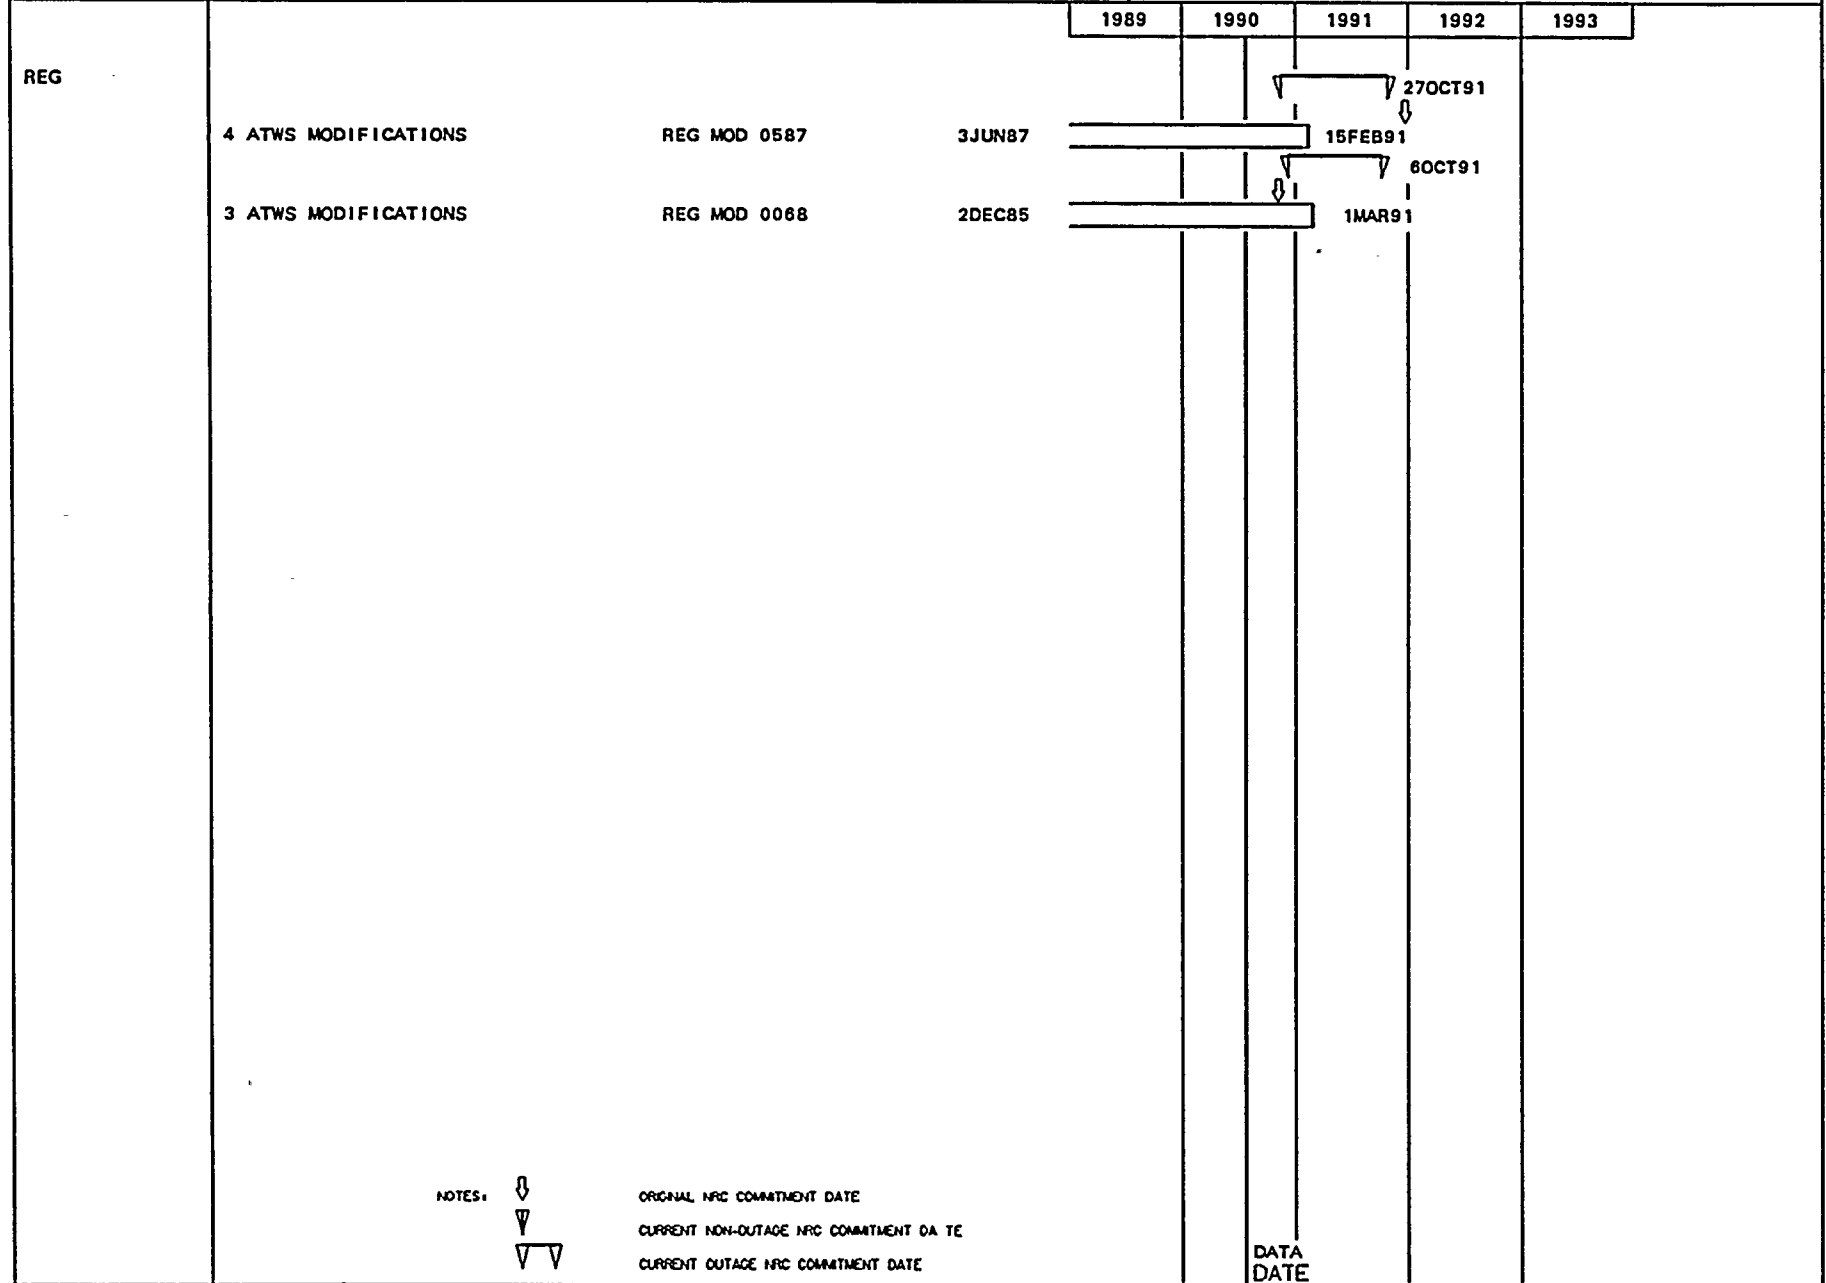




PROJECT ALMEGA99	TURKEY POINT NUCLEAR PLANT	MODE T/FT	TARGET SCHEDULE 30	RLM 2AUG90 14 88
PLOT NRR	INTEGRATED SCHEDULE	INTERVAL 1 YEAR(S)	TARG FINISH 17MAY95	PROJECT/2 8683
PAGE 1 SHEET 1	FLORIDA POWER AND LIGHT CO.		TARG DATA DATE 29NOV88	SCHEDULE BAR CHART
START 2JAN84	T A R G E T S C H E D U L E	SHORT BREAKS CODES 9	CUR EF	
FINISH 15AUG95	PAGE BREAK VALUE: 3 - NRR			
DATA DATE 25JUN90	LINE BREAK ON NRC COMMITMENT CATEGORIES			

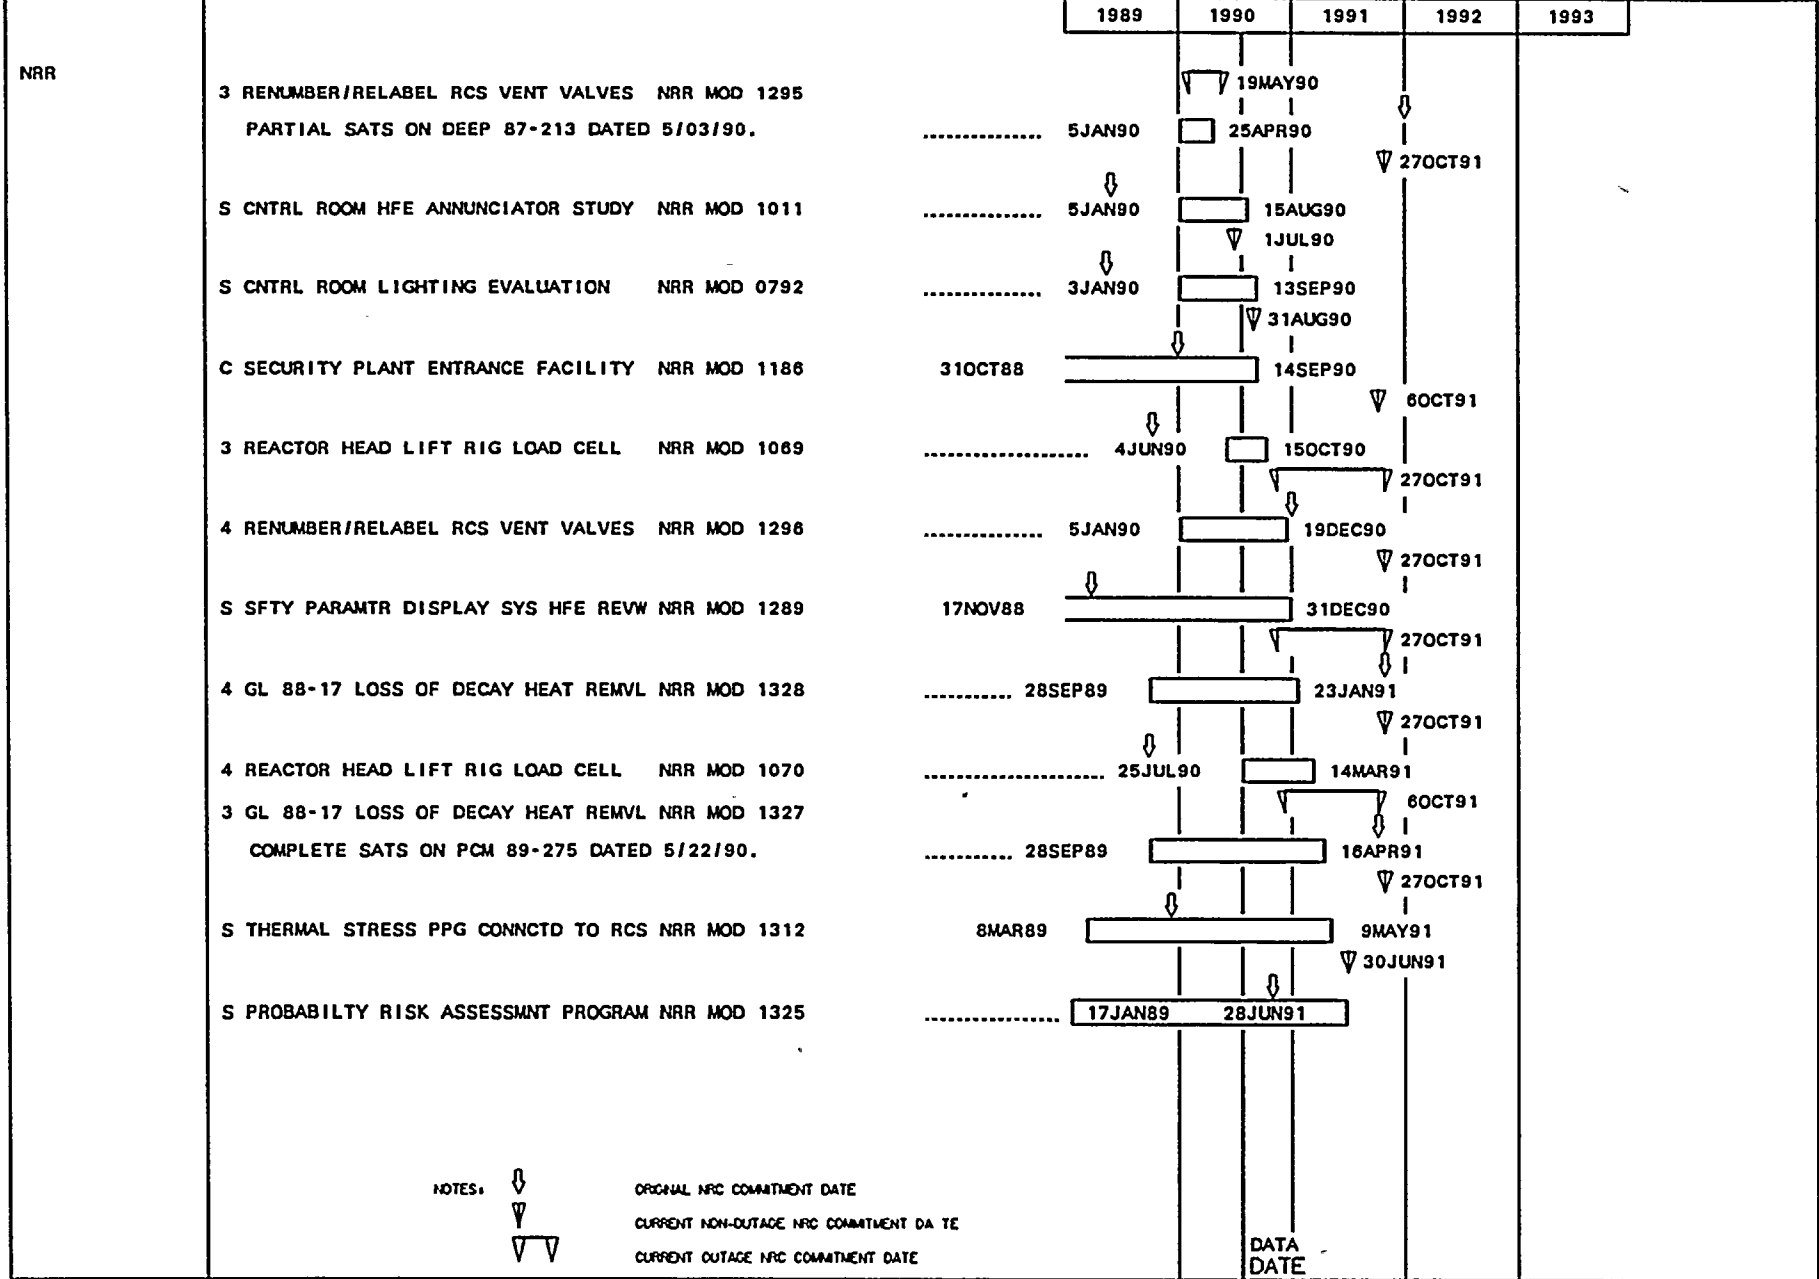

4.

PROJECT ALMEGA99	TURKEY POINT NUCLEAR PLANT	MODE T/FF	TARGET SCHEDULE 30	DIR 24JUN90 16-88
PIOT NRR	INTEGRATED SCHEDULE	INTERVAL: 1 YEAR(S)	TARG FINISH 17MAY95	PROJECT# 8683
PAGE 1 SHEET 2	FLORIDA POWER AND LIGHT CO.	START BREAKS CODES 9	TARG DATA DATE 29NOV88	SCHEDULE BAR CHART
START 22JAN84	T A R G E T S C H E D U L E	CUR EF		
FINISH 16AUG95	PAGE BREAK VALUE: 3 - NRR			
DATA DATE 24JUN 90	LINE BREAK ON NRC COMMITMENT CATEGORIES			

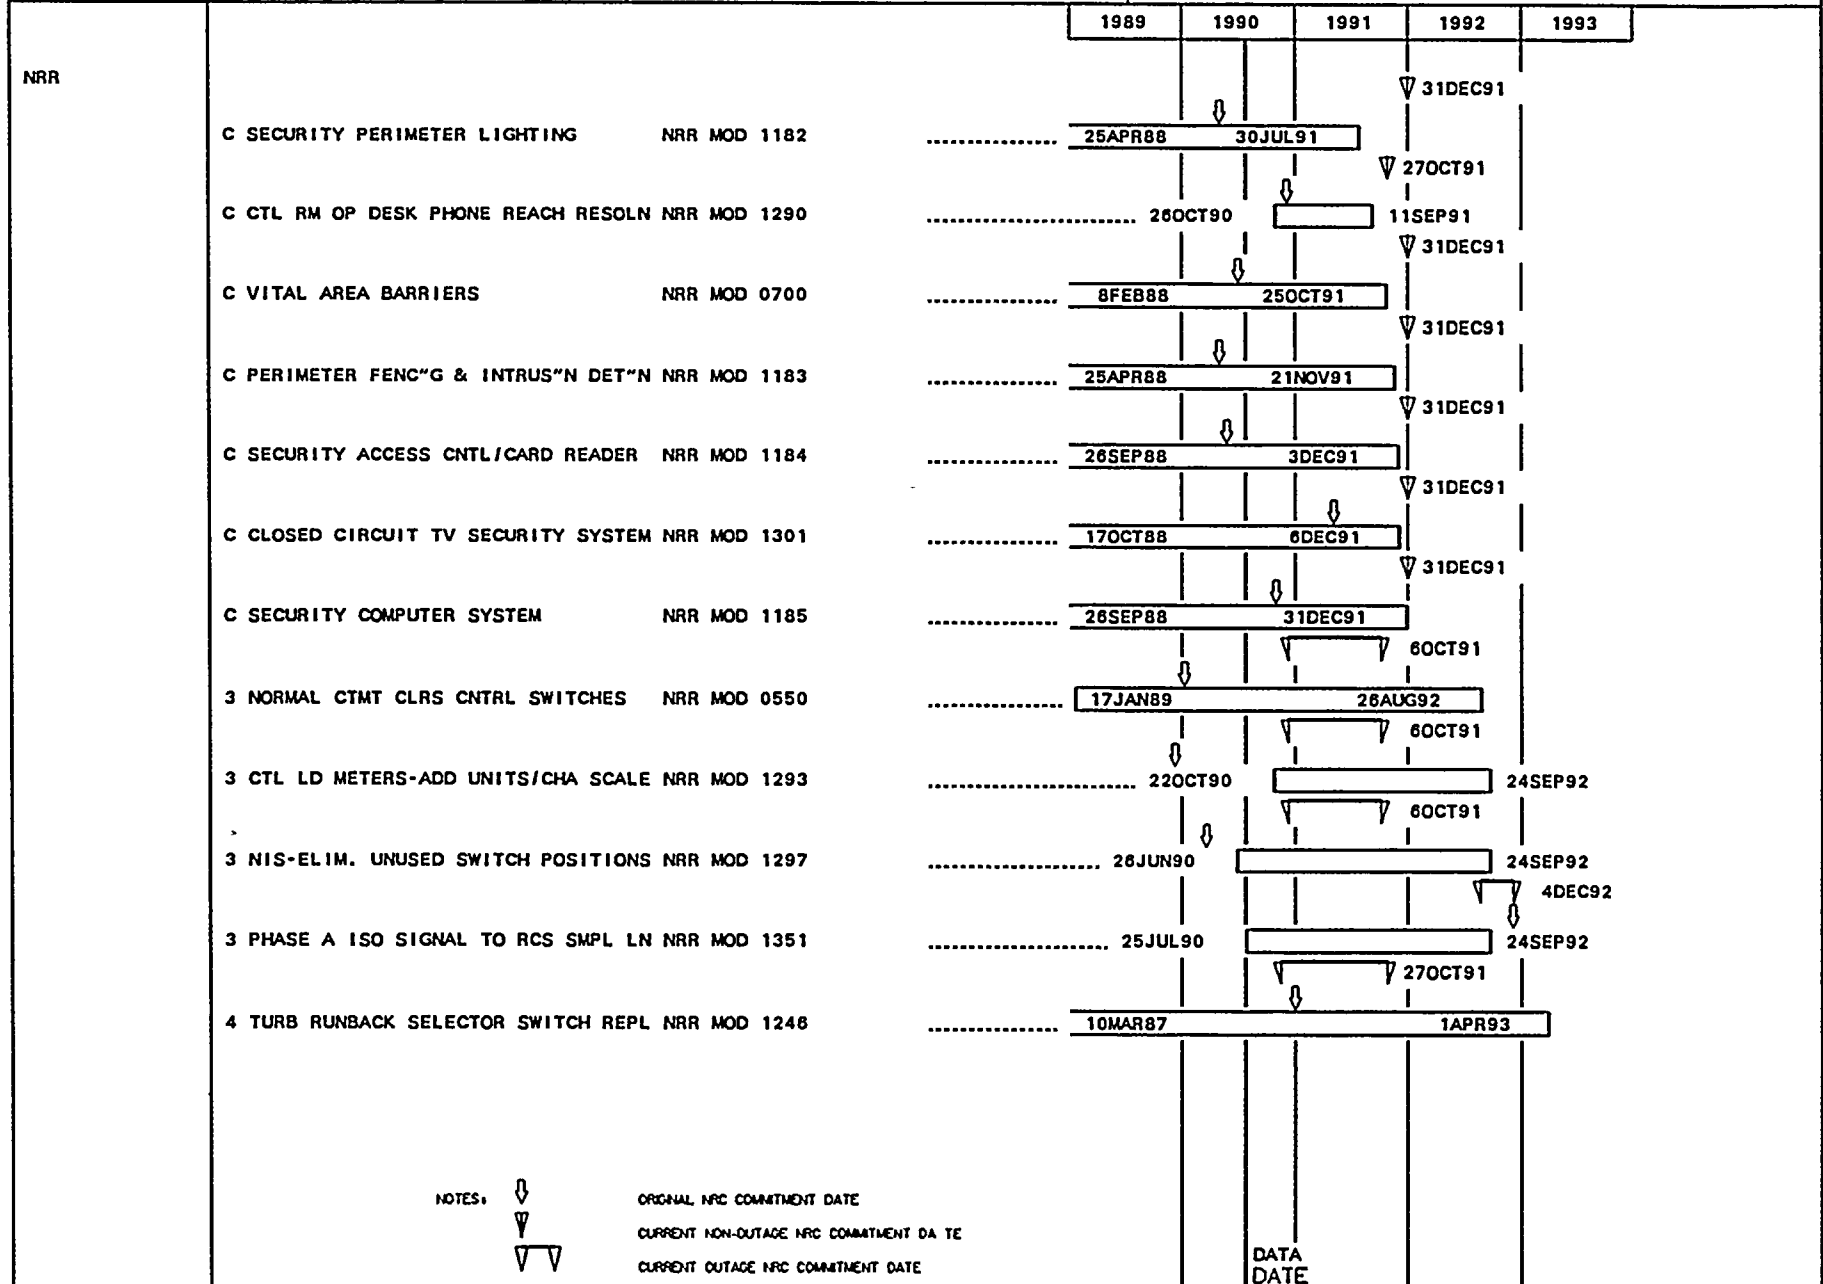




12

12

PROJECT ALMEGA99	TURKEY POINT NUCLEAR PLANT	MODE TIFT	TARGET SCHEDULE 20	RUN 24JUN90 14.55
PIOT NRR	INTEGRATED SCHEDULE	INTERVAL: 1 YEAR(S)	TARG FINISH 17MAY95	PROJECT# 8483
PAGE 1 SHEET 3	FLORIDA POWER AND LIGHT CO.		TARG DATA DATE 29NOV88	SCHEDULE BAR CHART
START 23AN84	T A R G E T S C H E D U L E	SHORT BREAKS BCODES 9	CUR EF	
FINISH 16AUG95	PAGE BREAK VALUE: 3 - NRR			
DATA DATE 24JUN90	LINE BREAK ON NRC COMMITMENT CATEGORIES			

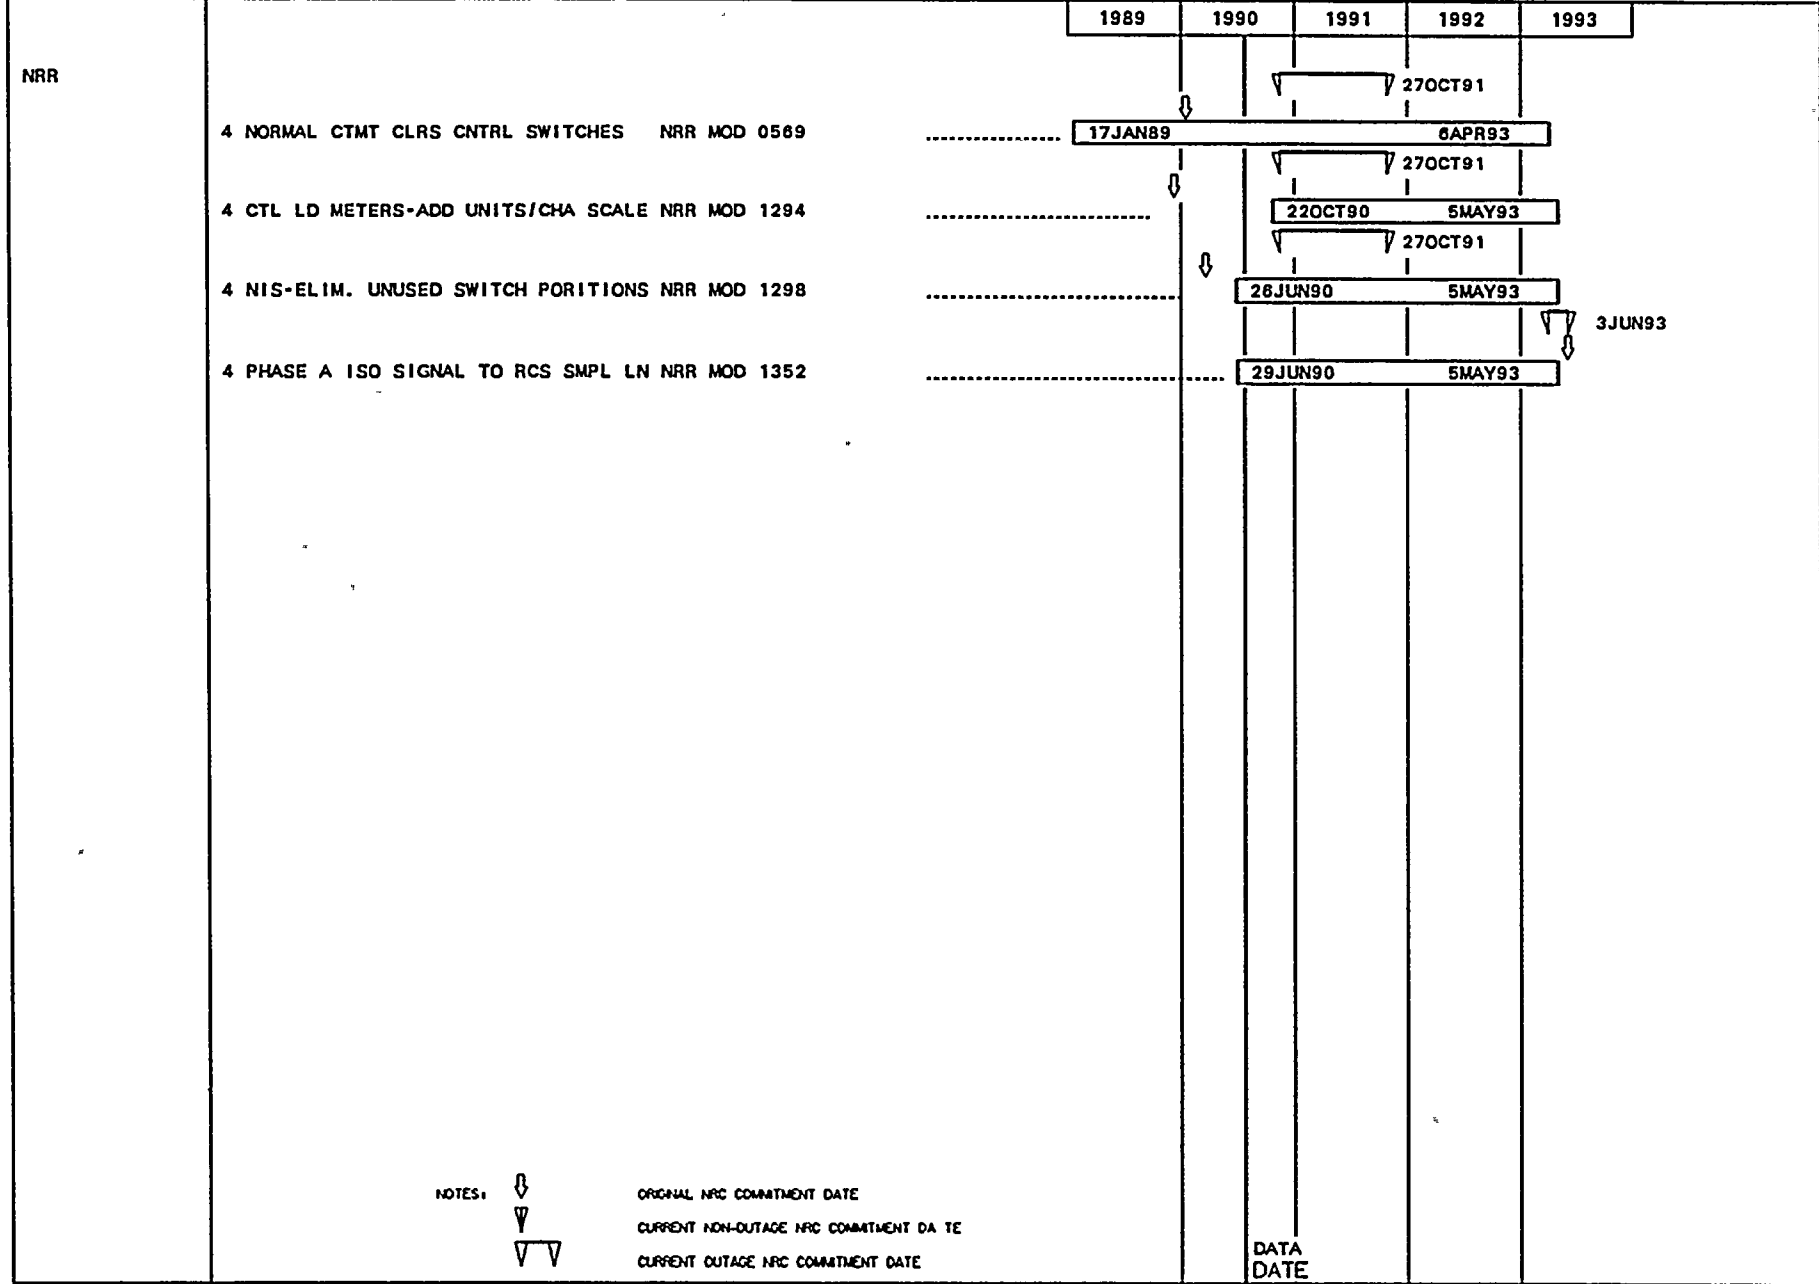




☆

.....




PROJECT ALMEGA99	TURKEY POINT NUCLEAR PLANT	MODE T/FT	TARGET SCHEDULE 30	RUN 24JUN90 14-67
PLOT I&E	INTEGRATED SCHEDULE	INTERVAL: 1 YEAR(S)	TARG FINISH 17MAY95	PROJECT# 8483
PAGE 1 SHEET 1	FLORIDA POWER AND LIGHT CO.		TARG DATA DATE 29NOV88	SCHEDULE BAR CHART
START 22JAN84	T A R G E T S C H E D U L E	SHORT BREAKS CODES 9	CUR EF	
FINISH 16AUG95	PAGE BREAK VALUE: 4 - I&E			
DATA DATE 26JUN90	LINE BREAK ON NRC COMMITMENT CATEGORIES			

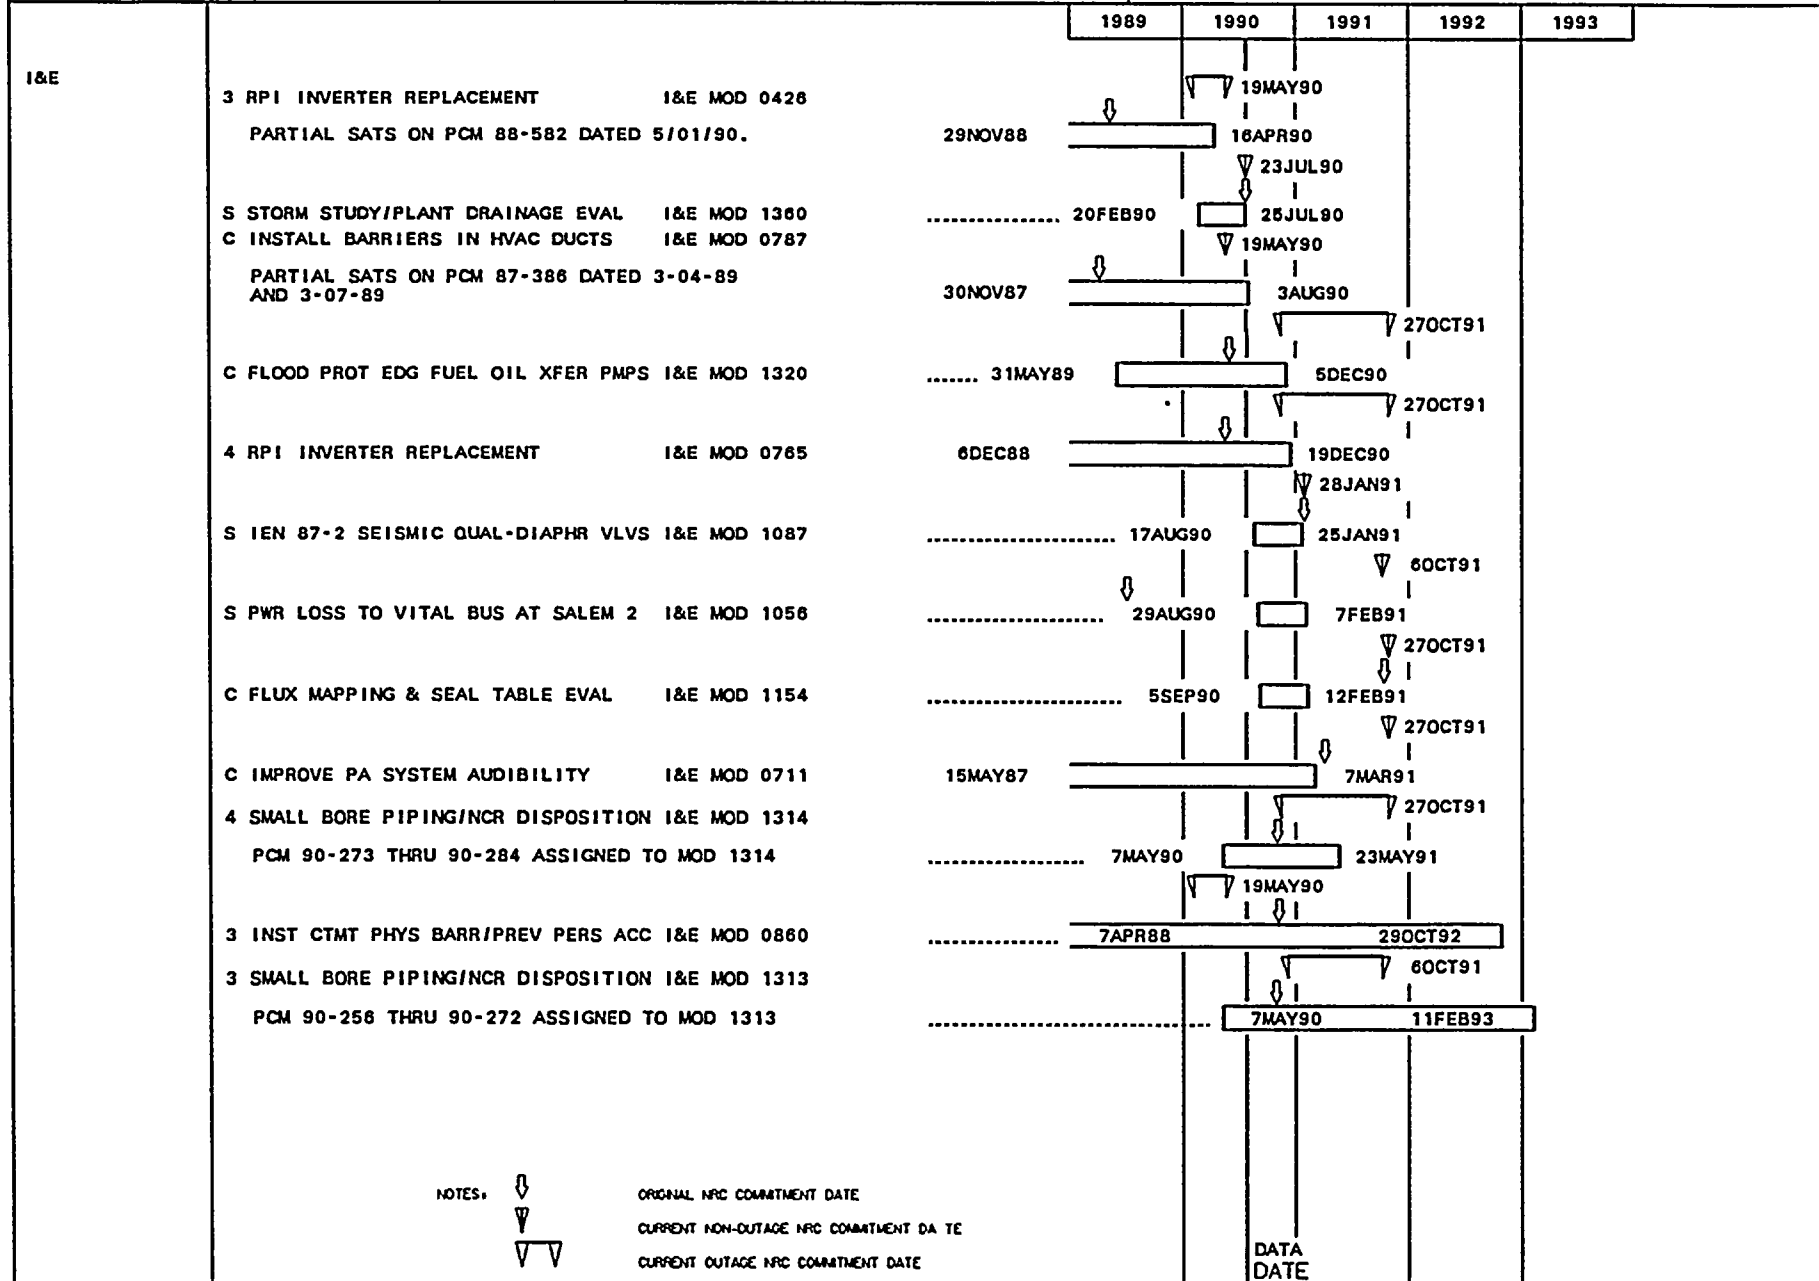





12






PROJECT ALMEG89	TURKEY POINT NUCLEAR PLANT	MODE 1/FT	TARGET SCHEDULE 30	BLN 2AUG90 18:58
PLOT ORA	INTEGRATED SCHEDULE	INTERVAL 1 YEAR(S)	TARG FINISH 17MAY95	PROJECT# 8483
PAGE 1 SHEET 1	FLORIDA POWER AND LIGHT CO.		TARG DATA DATE 29NOV88	SCHEDULE BAR CHART
START 22JAN84	T A R G E T S C H E D U L E	SHORT BREAKS CODES 9	CUR EF	
FINISH 16AUG95	PAGE BREAK VALUE: 6 - ORA			
DATA DATE 24JUL90	LINE BREAK ON NRC COMMITMENT CATEGORIES			

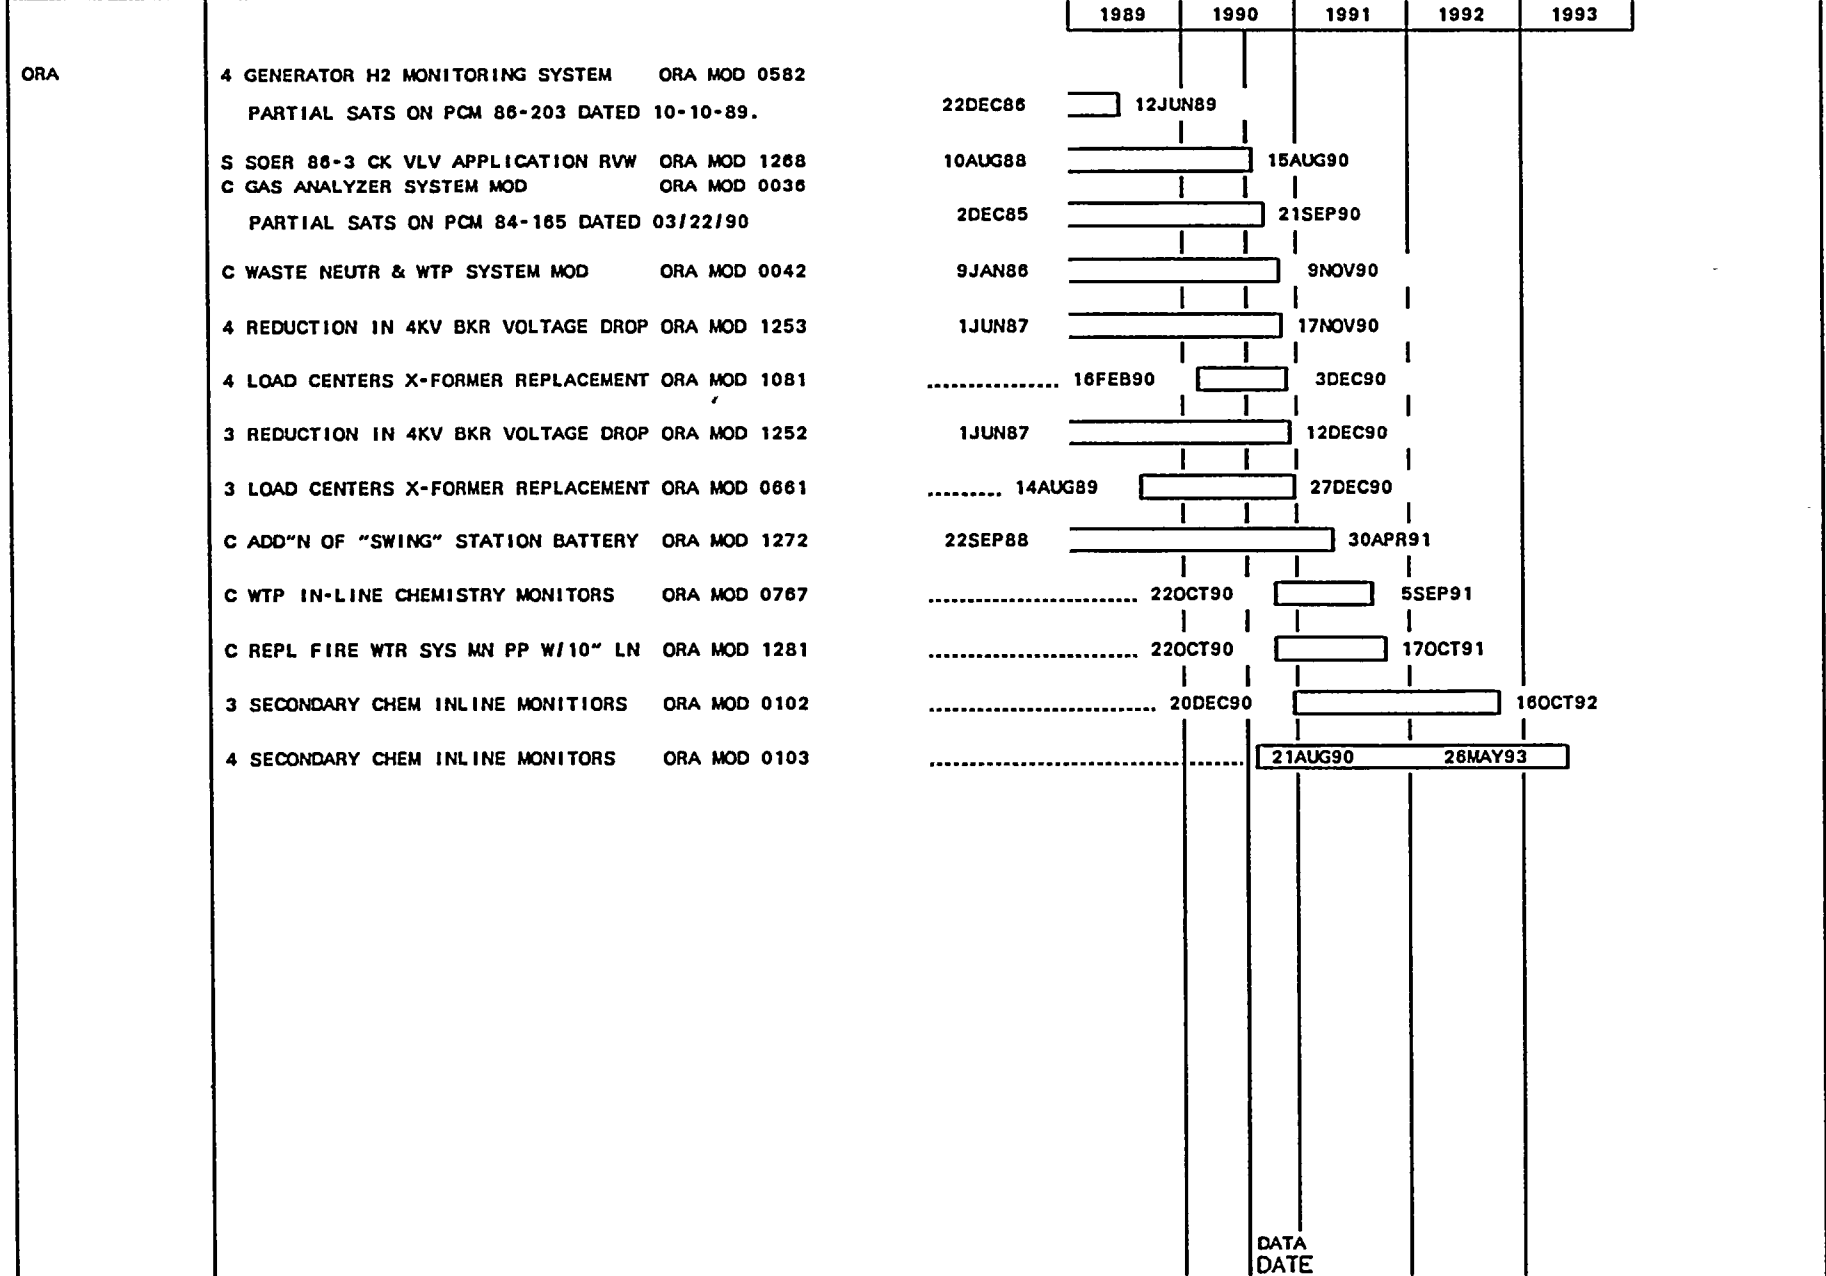









PROJECT ALMEGA99 PLOT FPL	TURKEY POINT NUCLEAR PLANT INTEGRATED SCHEDULE FLORIDA POWER AND LIGHT CO.	MODE T/FT INTERVAL 1 YEAR(S)	TARGET SCHEDULE 30 TARG FINISH 17MAY95 TARG DATA DATE 29NOV88	RUN 2ALIG90 15-00 PROJECT# 8681 SCHEDULE BAR CHART	
PAGE 1 SHEET 2	T A R G E T S C H E D U L E	START BREAKS CODES 9	CUR EF		
START 2JAN84 FINISH 16AUG95 DATA DATE 24JUN90	PAGE BREAK VALUE: 5 - FPL LINE BREAK ON NRC COMMITMENT CATEGORIES				
				1989 1990 1991 1992 1993	
FPL	S ICW CK VLV OPER W/IA FAILURE FPL MOD 1283 NEED ENGINEERING LETTER FOR CLOSURE. 3 AFW FLOW TRANSMITTER REPLACEMENT FPL MOD 0250 COMPLETE SATS ON PCM 90-088 DATED 07-13-90 3 PZR RLF LN SNUBBER REPLACEMENT FPL MOD 1267 PARTIAL SATS ON PCM 89-046 DATED 04/16/90 3 MSIV AIR OPERATOR BACKUP N2 SYST FPL MOD 0267 SATS REQUIRED FOR CLOSURE. S ACCEPTABILITY OF DC EQUIP RATINGS FPL MOD 0404 COMPLETE PER LETTER JPN-PTP-89-2521. 3 ATMOSPHERIC DUMP VLV REPLACEMENT FPL MOD 1259 PARTIAL SATS ON PCM 88-517 DATED 05-11-90 AND 07-16-90 3 SI ACCUM LVL TRANSMITTER PLATFORM FPL MOD 1350 COMPLETE SATS ON PCM 89-500 DATED 07-18-90 3 SGWL CNTMT ISOLAT'N VLV REPLACENT FPL MOD 0293 PARTIAL SATS ON PCM 86-077 DATED 6/13/90. 3 NORM CNTMT CLRS CAPACITY INCREASE FPL MOD 0902 PARTIAL SATS ON PCM 87-025 DATED 07-16-90 S METEOROLOGICAL SYSTEMS EVALUATION FPL MOD 1053 COMPLETE PER LETTER JPN-PTP-90-1670. 4 BACKUP INSTR. AIR COMPRESSOR FPL MOD 0291 SATS REQUIRED FOR CLOSURE. C PASS CHLORIDE ANALYZER REPLACMNT FPL MOD 1319 3 MSR MODERNIZATION REPLACEMENT FPL MOD 0050 PARTIAL SATS ON PCM 85-132 DATED 07-02-87. 3 BORIC ACID EVAP PMP UPGRADE FPL MOD 0237 NEED SATS FOR CLOSURE 3 MAIN STM SAFETY LIFTING LEVERS FPL MOD 0422 SATS REQUIRED FOR CLOSURE. 3 ADD'L CNTMT ELECT PENETRATIONS FPL MOD 0549 PARTIAL SATS ON PCM 89-335 - 3/22/90 & 5/1/90 S MOV THERMAL OVERLOAD HTR SELECTN FPL MOD 1249 REF. LTR JPE-PT-P-88-1051 CONFIRMS MEETING NRC COMMIT ON JUN 20, 1988. COMPLETION OF PREP & APPVL OF STD E-3.20 MEETS NRC COMMITMENT. EP TO BE ISS SPECIFYING TOL'S FOR MOV'S. IS NOT NRC COMMITMENT RELATED. 3 INSPECT/REPAIR INTAKE STRUCTURE FPL MOD 1348	26OCT87 3JUN86 5OCT88 2DEC85 11JAN88 3MAY88 ..... 2OCT89 21MAR86 23JAN89 ..... 1SEP89 4APR86 ..... 31MAY89 2DEC85 12NOV85 17APR86 15FEB89 19OCT87 ..... 30OCT89	10APR90 11APR90 18APR90 23APR90 27APR90 21MAY90 21MAY90 22MAY90 29MAY90 4JUN90 24JUL90 24JUL90 25JUL90 25JUL90 25JUL90 25JUL90 25JUL90 25JUL90		
				DATA DATE	



100

5

A

4

10

10

4

100

100

100

100

100

PROJECT ALMEGAS9	TURKEY POINT NUCLEAR PLANT	MODE T/J/T	TARGET SCHEDULE 30	RUN 2AUG90 15:00
PLOT FPL	INTEGRATED SCHEDULE	INTERVAL 1 YEAR(S)	TARG FINISH 17MAY95	PROJECT/2 8683
PAGE 1 SHEET 3	FLORIDA POWER AND LIGHT CO.		TARG DATA DATE 29NOV88	SCHEDULE BAR CHART
START 23JAN84	T A R G E T S C H E D U L E	SOFT BREAKS BCODES 9	CUR EF	
FINISH 16AUG95	PAGE BREAK VALUE: 5 = FPL			
DATA DATE 28JUL90	LINE BREAK ON NRC COMMITMENT CATEGORIES			


		1989	1990	1991	1992	1993
FPL	4 ADD & RELOCATE AFW N2 SUPPLY FPL MOD 0216					
	COMPLETE SATS ON PCM 85-178 DATED 06-27-87. COMPLETE SATS ON PCM 88-045 DATED 04-04-88. PARTIAL SATS ON PCM 88-184 DATED 04-21-89.	2DEC85		27JUL90		
	3 REMOVAL OF TPCW AMERTAP SYSTEM FPL MOD 1317 TPCW AMERTAP SYSTEM WORK WAS SPLIT FROM MOD 531. TPCW AMERTAP WAS NOT NRC COMMITMENT RELATED.	18NOV86		3AUG90		
	4 TPCW HX ISOLTN - CV2201 FAIL CLSE FPL MOD 1285 PARTIAL SATS ON PCM 88-346 DATED 04-29-89.	15NOV88		8AUG90		
	3 CHARG PUMP SUCTN QUICK DISCONNECT FPL MOD 0431	22DEC86		7AUG90		
	4 CHARG PUMP SUCTN QUICK DISCONNECT FPL MOD 1255	22DEC86		7AUG90		
	C W.T.P. FLOW METERS UPGRADE FPL MOD 0151	11FEB86		8AUG90		
	3 REPL CCW HX THERMOMETERS W/RTD'S FPL MOD 0417 SATS REQUIRED FOR CLOSURE.	30MAR87		10AUG90		
	4 REPL TUBE SIDE CCW HX TIS W/RTD'S FPL MOD 0418	15APR87		10AUG90		
	S ICW PMP FDN SFTY HAZARD EVALUAT'N FPL MOD 1310	..... 1FEB90		10AUG90		
	C REG GUIDE 1.97 AUDIT PREP FPL MOD 1326	..... 17AUG89		17AUG90		
	4 CHEM INJECTION OF ICW TO CCW HX FPL MOD 1322 3 PORV STROKE TIME ENHANCEMENT FPL MOD 1315 PARTIAL SATS ON PCM 89-585 DATED 04/18/90	..... 5JUN89		22AUG90		
	24OCT88			24AUG90		
	S RESOLVE CNTMT PURG FSAR DISCREP FPL MOD 0828	..... 17NOV89		27AUG90		
	S BOUNDARIES FOR VISUAL LEAK INSP FPL MOD 0396 C CONTROL ROOM HABITABILITY HVAC FPL MOD 0014 THE COMMITMENT RELATED PORTION OF THIS MODIFICATION HAS BEEN COMPLETED. ENHANCEMENTS TO THE CONTROL ROOM HVAC SYST. BEYOND 17 JUN 88 ARE NOT CFO RELATED.	16JAN87		6SEP90		
	2JAN85			10SEP90		
	4 HIGH INITIAL RESPONSE EXCITER FPL MOD 0979 PARTIAL SATS ON PCM 86-201 DATED 05-22-89.	9FEB87		13SEP90		
	4 SFP DEMIN RESIN FLUSH UPGRADE FPL MOD 1155	19OCT87		14SEP90		
	3 SFP DEMIN RESIN FLUSH UPGRADE FPL MOD 0956	6OCT87		18SEP90		

DATA DATE




2  
3  
4  
5  
6  
7  
8  
9  
10  
11  
12  
13  
14  
15  
16  
17  
18  
19  
20  
21  
22  
23  
24  
25  
26  
27  
28  
29  
30  
31  
32  
33  
34  
35  
36  
37  
38  
39  
40  
41  
42  
43  
44  
45  
46  
47  
48  
49  
50  
51  
52  
53  
54  
55  
56  
57  
58  
59  
60  
61  
62  
63  
64  
65  
66  
67  
68  
69  
70  
71  
72  
73  
74  
75  
76  
77  
78  
79  
80  
81  
82  
83  
84  
85  
86  
87  
88  
89  
90  
91  
92  
93  
94  
95  
96  
97  
98  
99  
100

PROJECT ALMEG99 PLOT FPL PAGE 1 SHEET 4		TURKEY POINT NUCLEAR PLANT INTEGRATED SCHEDULE FLORIDA POWER AND LIGHT CO.		MODE T/FT INTERVAL: 1 YEAR(S)	TARGET SCHEDULE 30 TARG FINISH 17MAY95 TARG DATA DATE 28NOV88	BLN 2ALIC90 15:00 PROJECT# 8683 SCHEDULE BAR CHART					
START 2JAN84 FINISH 18AUG95 DATA DATE 28JUN90		T A R G E T S C H E D U L E		SHORT BREAKS BCODES 9	CUR EF						
		PAGE BREAK VALUE, S - FPL									
		LINE BREAK ON NRC COMMITMENT CATEGORIES									
					1989	1990	1991	1992	1993		
FPL	3 MSR INSTRUMENTATION	FPL MOD 1010	26JUN87	[Bar]		25SEP90					
	4 SPENT FUEL POOL RERACKING	FPL MOD 1190	31JUL87	[Bar]		20OCT90					
	PARTIAL SATS ON PCM 87-405 DATED 12-01-89		31JUL87	[Bar]		20OCT90					
	C NEW EDG FIRE PROTECTION	FPL MOD 1176	11MAY88	[Bar]		30OCT90					
	3 SFP BRIDGE CRANE REPLACEMENT	FPL MOD 0745	20JAN88	[Bar]		9OCT90					
	S REVIEW WEJ-IT EXPANSION ANCHORS	FPL MOD 0586	4MAY87	[Bar]		18OCT90					
	4 SFP BRIDGE CRANE REPLACEMENT	FPL MOD 0744	4FEB88	[Bar]		22OCT90					
	S BKR LIST VERIF" N WALKDOWN OF NCRS	FPL MOD 1265	8FEB89	[Bar]		25OCT90					
	THE COMMITMENT RELATED PORTION OF THIS MOD HAS BEEN COMPLETED PER LTR JPN-PTP-90-0190, DATED 1/19/90. THE REMAINDER OF THE WORK IS NOT CFO RELATED. COMPLETE SATS ON PCM 89-323 DATED 6/14/90.		8FEB89	[Bar]		25OCT90	22JAN91				
	C EDG PROJECT LICENSING SUBMITTALS	FPL MOD 1144	20JUL87	[Bar]		31OCT90					
	3 EDG STATION BATTERY CHARGERS	FPL MOD 1146	22MAR88	[Bar]		31OCT90					
	IMPLEMENTATION UNDER MOD #1145.		12JUN88	[Bar]		6NOV90					
	C ADD'L EMERG LIGHTING FOR APP. R	FPL MOD 0592	12JUN88	[Bar]		6NOV90					
	PARTIAL SATS ON PCM 88-213 (REV 6) 10-31-89 MOD IS ON REV 8 ( AS OF 5/10/90 ).		12JUN88	[Bar]		6NOV90					
	4 MAIN FEED CV 2011 CLOSING TIME	FPL MOD 1102	9MAR88	[Bar]		17NOV90					
	3 POLAR CRANE MOTORS/ENGR PACKAGE	FPL MOD 0476	25JUL90	[Bar]		21NOV90					
	4 POLAR CRANE MOTORS/ENGR PACKAGE	FPL MOD 0477	25JUL90	[Bar]		21NOV90					
	4 MG-6 RELAY REPLACEMENT	FPL MOD 1354	13FEB90	[Bar]		21NOV90					
	4 REACTOR CAVITY HANDRAIL	FPL MOD 0080	2MAR87	[Bar]		26NOV90					
	4 EDG/LD CTR 4H, MCC4D & XFR OF LDS	FPL MOD 1139	10OCT88	[Bar]		26NOV90					
	IMPLEMENTATION UNDER MOD #1145.		10OCT88	[Bar]		26NOV90					
	3 EDG LOAD CTR 3H/MCC 3D	FPL MOD 1142	10OCT88	[Bar]		26NOV90					
	IMPLEMENTATION UNDER MOD #1145. PARTIAL SATS ON PCM 89-069 DATED 1/24/90 AND 2/14/90.		10OCT88	[Bar]		26NOV90					
					DATA DATE						



PROJECT ALMEGA99	TURKEY POINT NUCLEAR PLANT	MODE T/FT	TARGET SCHEDULE 30	RUN 2AUG90 15-00
PLOT FPL	INTEGRATED SCHEDULE	INTERVAL: 1 YEAR(S)	TARG FINISH 17MAY95	PROJECT/2 8683
PAGE 1 SHEET 6	FLORIDA POWER AND LIGHT CO.		TARG DATA DATE 28NOV88	SCHEDULE BAR CHART
START 23JAN84	T A R G E T S C H E D U L E	SOFT BREAKS #CODES 9	CUR EF	
FINISH 16AUG95	PAGE BREAK VALUE: 5 - FPL			
DATA DATE 28JUN90	LINE BREAK ON NRC COMMITMENT CATEGORIES			

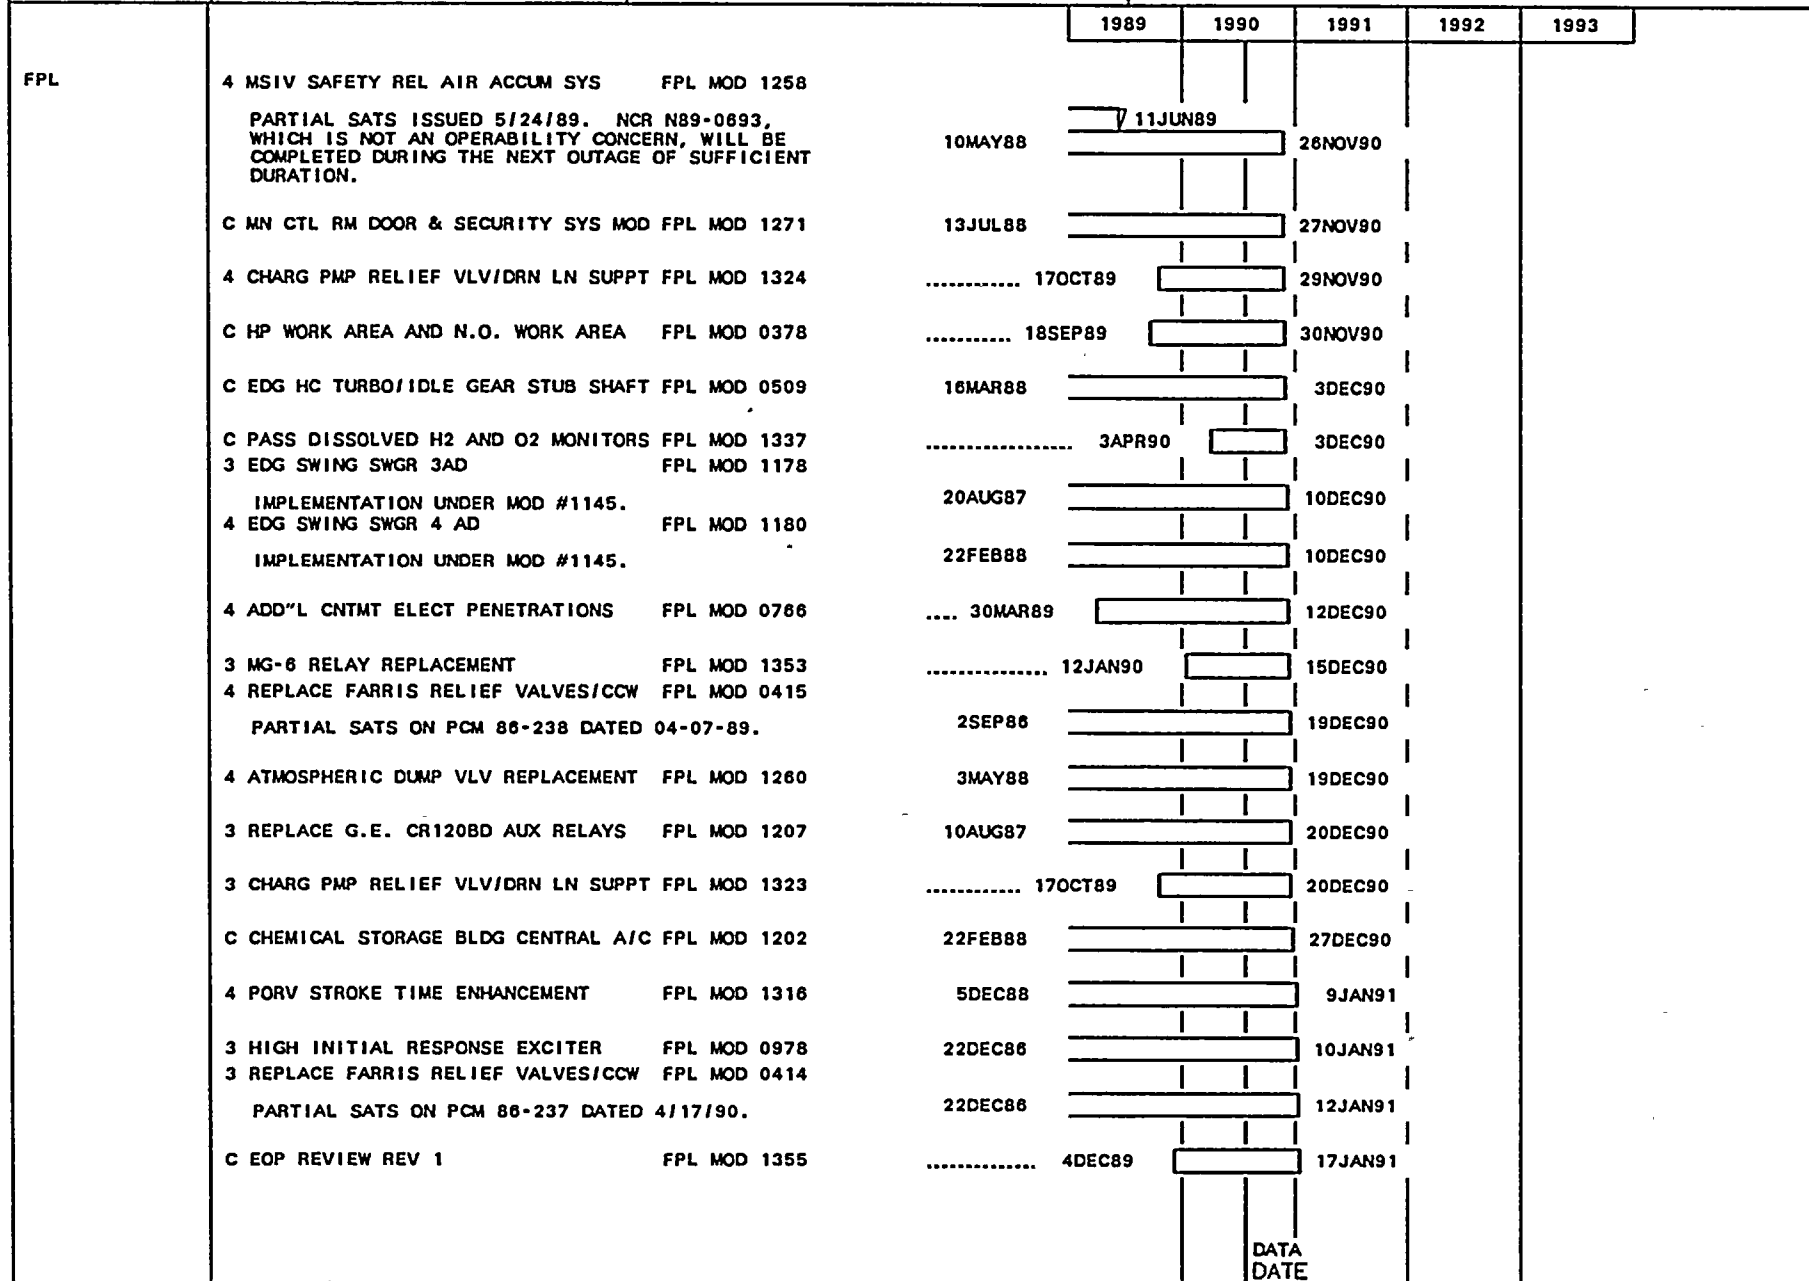




x

MA

9



PROJECT ALREGA99	TURKEY POINT NUCLEAR PLANT INTEGRATED SCHEDULE FLORIDA POWER AND LIGHT CO.	MODE T/IFF INTERVAL 1 YEAR(S)	TARGET SCHEDULE 30 TARG FINISH 17MAY95 TARG DATA DATE 29NOV88	RUN 2ALG98 15 00 PROJECT# 8483 SCHEDULE BAR CHART
PLOT FPL PAGE 1 SHEET 6	T A R G E T S C H E D U L E	SORT BREAKS @CODES 9	CUR EF	
START FINISH DATA DATE	21JAN86 16AUG95 24JUL90	PAGE BREAK VALUE: 5 - FPL LINE BREAK ON MRC COMMITMENT CATEGORIES		

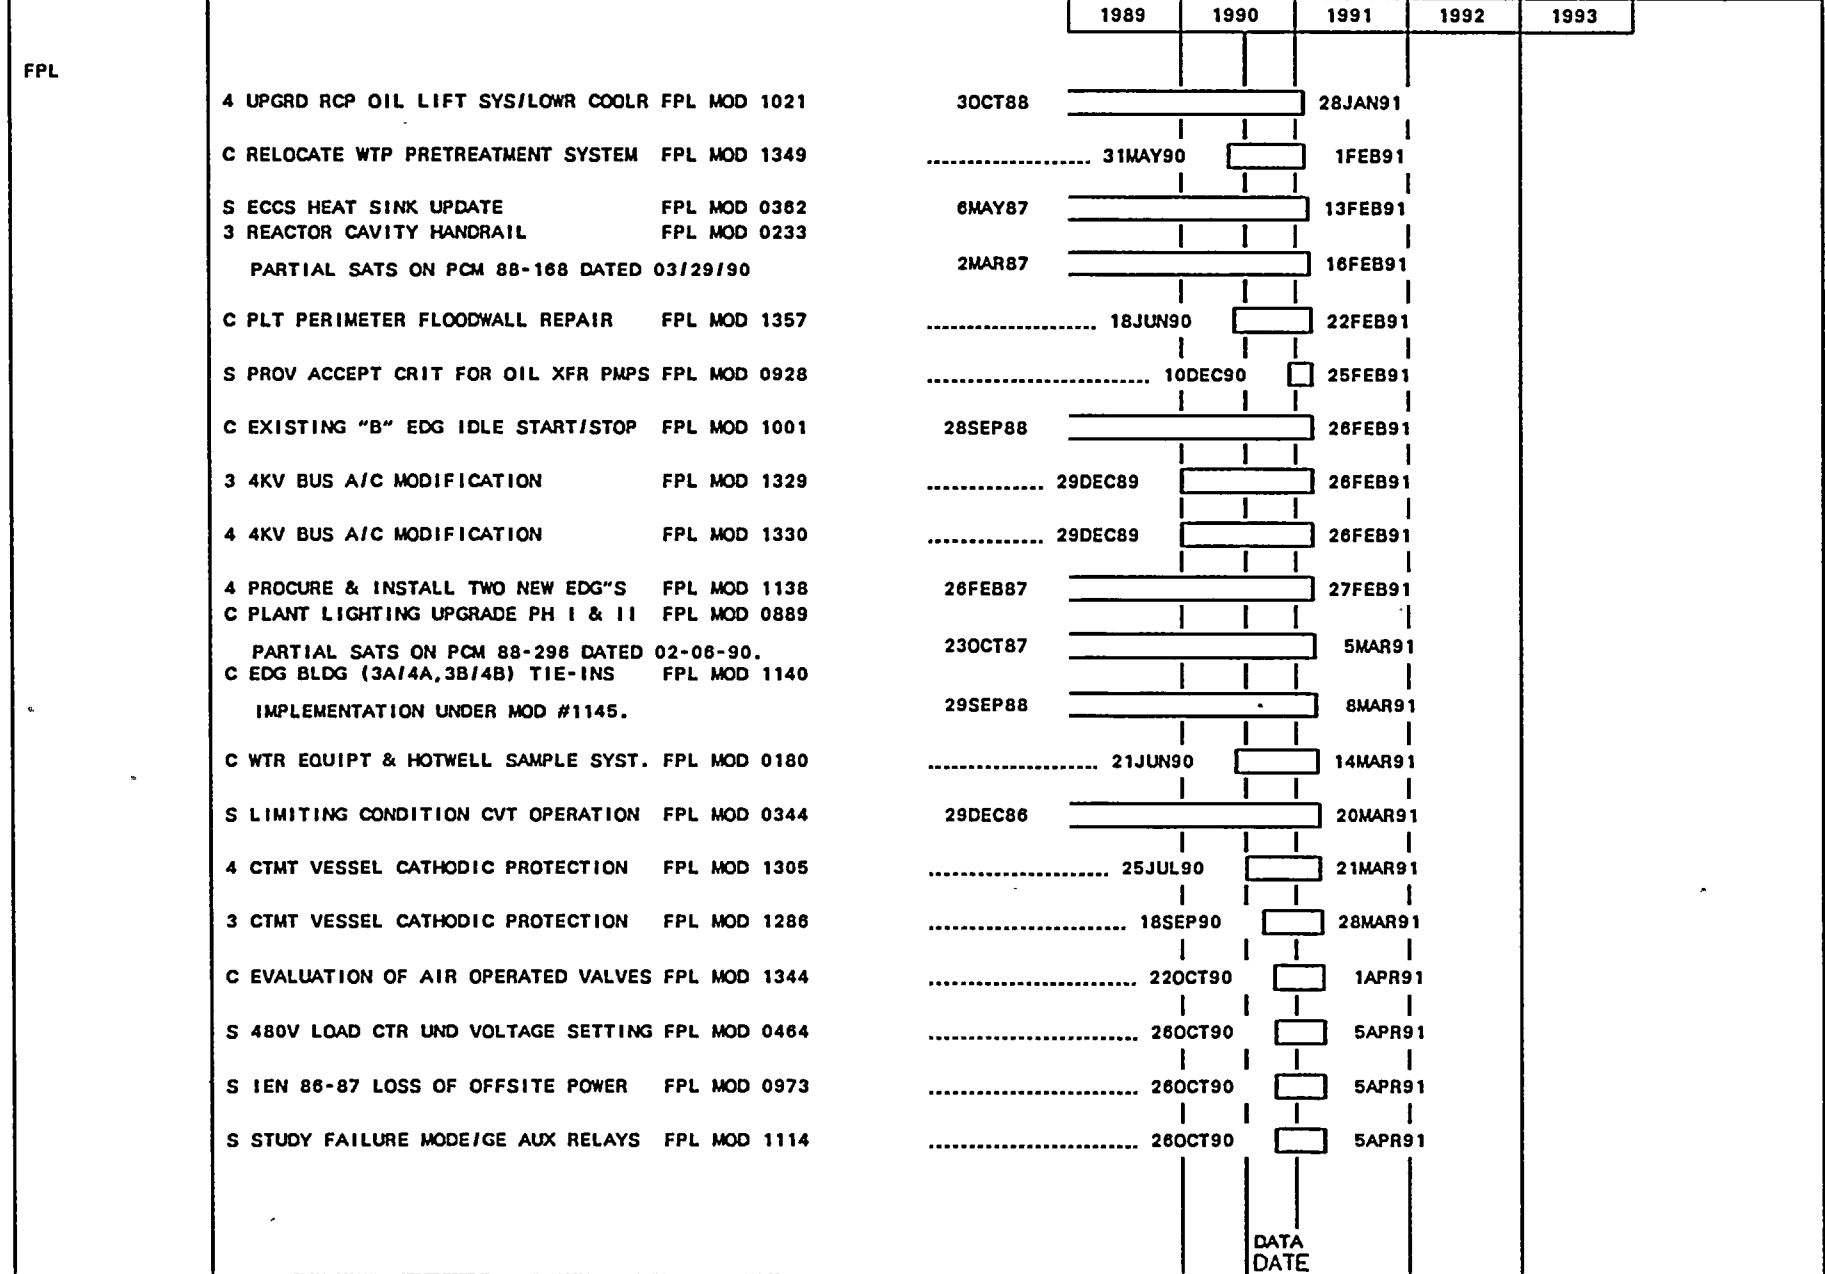

12. 9. 16




1-2-2

ME

1 2 3 4 5 6 7 8 9 10 11 12

13

PROJECT ALHGA99 FLOT FPL	TURKEY POINT NUCLEAR PLANT INTEGRATED SCHEDULE FLORIDA POWER AND LIGHT CO.	MODE T/FT INTERVAL 1 YEAR(S)	TARGET SCHEDULE 30 TARG FINISH 17MAY95 TARG DATA DATE 29NOV88	RUN 24JUN90 15.00 PROJECT 2 8483 SCHEDULE BAR CHART
PAGE 1 SHEET 7	T A R G E T S C H E D U L E	SOFT BREAKS @CODES 9	CUR EF	
START 22JAN84 FINISH 16AUG95 DATA DATE 24JUN90	PAGE BREAK VALUE: 5 - FPL LINE BREAK ON NRC COMMITMENT CATEGORIES			

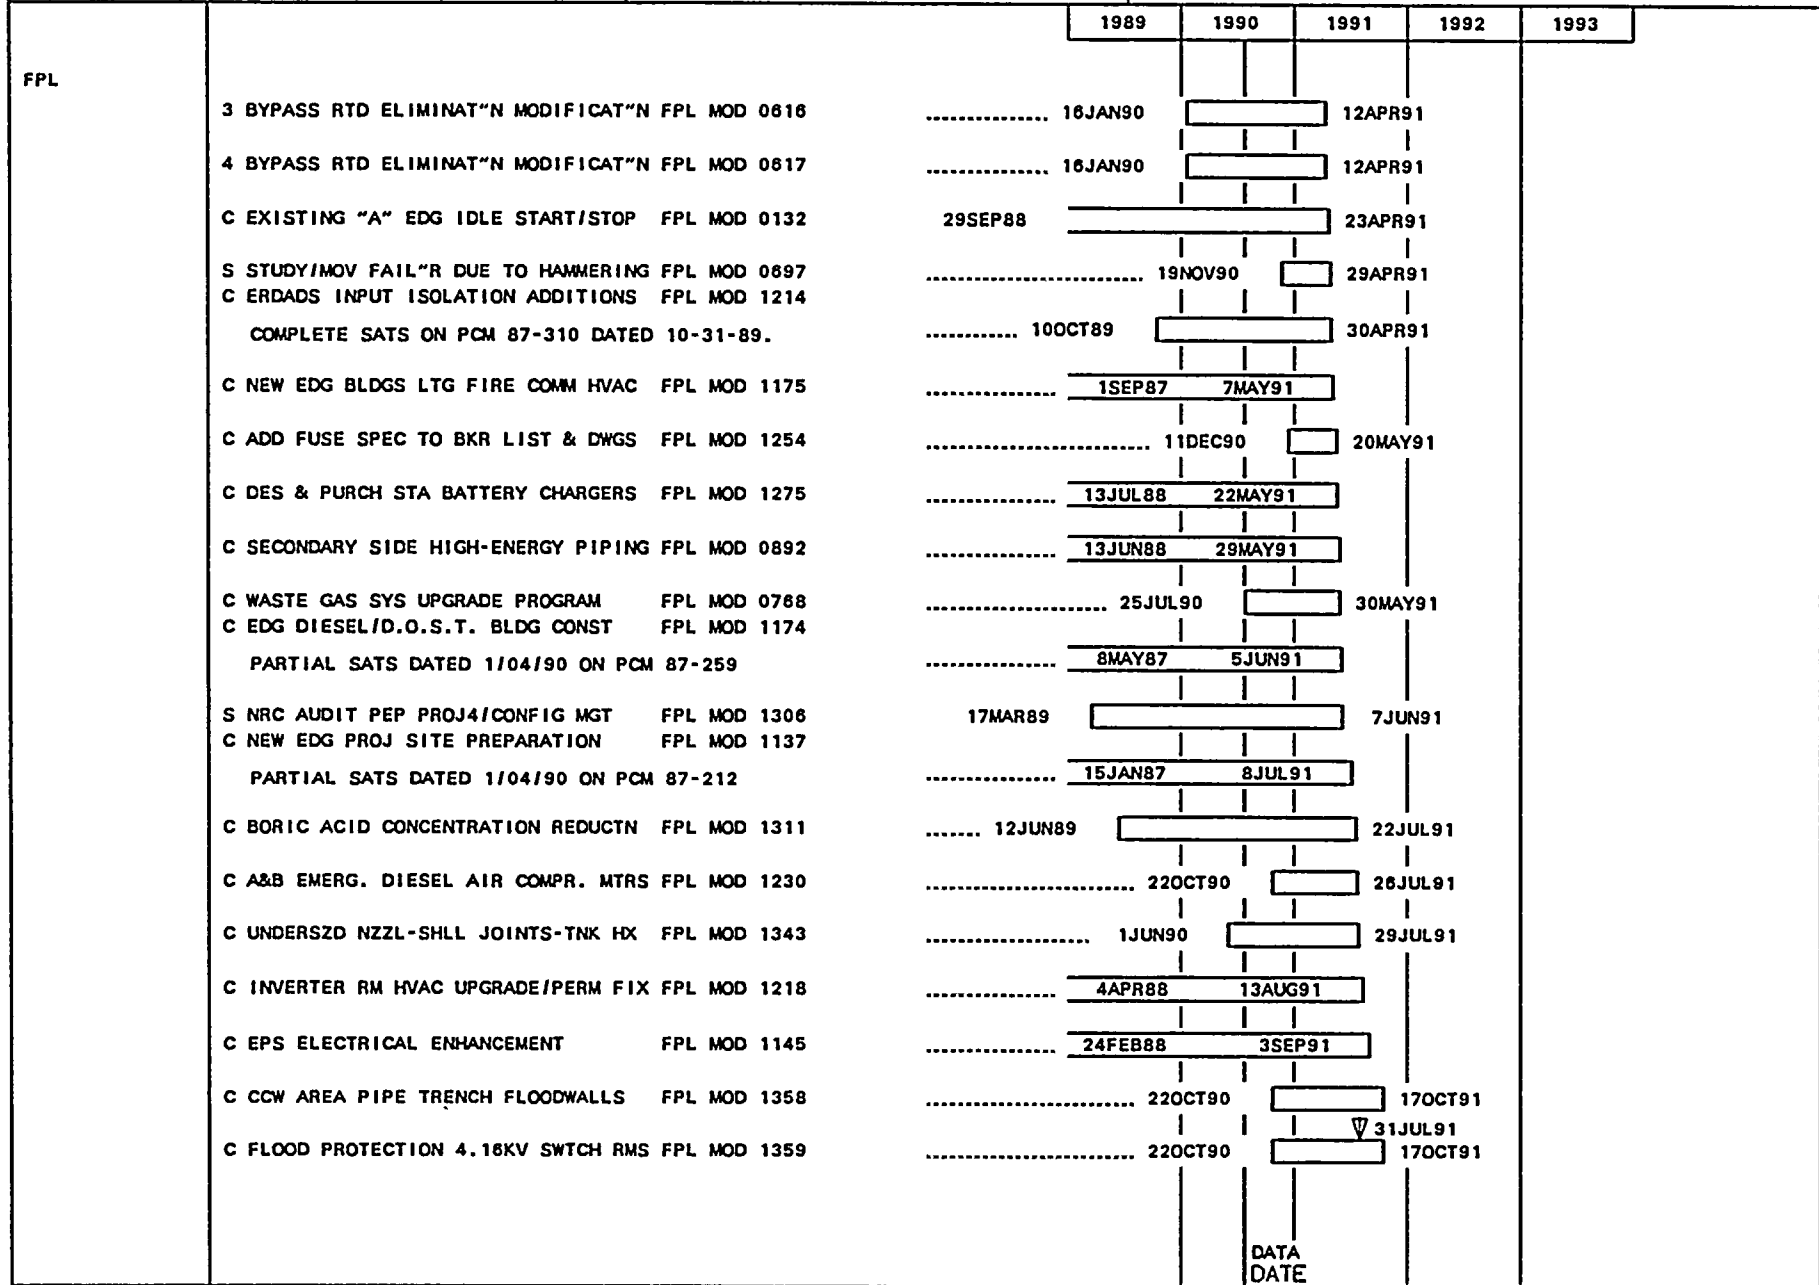


1  
2  
3  
4  
5  
6  
7  
8  
9  
10  
11  
12  
13  
14  
15  
16  
17  
18  
19  
20  
21  
22  
23  
24  
25  
26  
27  
28  
29  
30  
31  
32  
33  
34  
35  
36  
37  
38  
39  
40  
41  
42  
43  
44  
45  
46  
47  
48  
49  
50  
51  
52  
53  
54  
55  
56  
57  
58  
59  
60  
61  
62  
63  
64  
65  
66  
67  
68  
69  
70  
71  
72  
73  
74  
75  
76  
77  
78  
79  
80  
81  
82  
83  
84  
85  
86  
87  
88  
89  
90  
91  
92  
93  
94  
95  
96  
97  
98  
99  
100

101


102

103


104

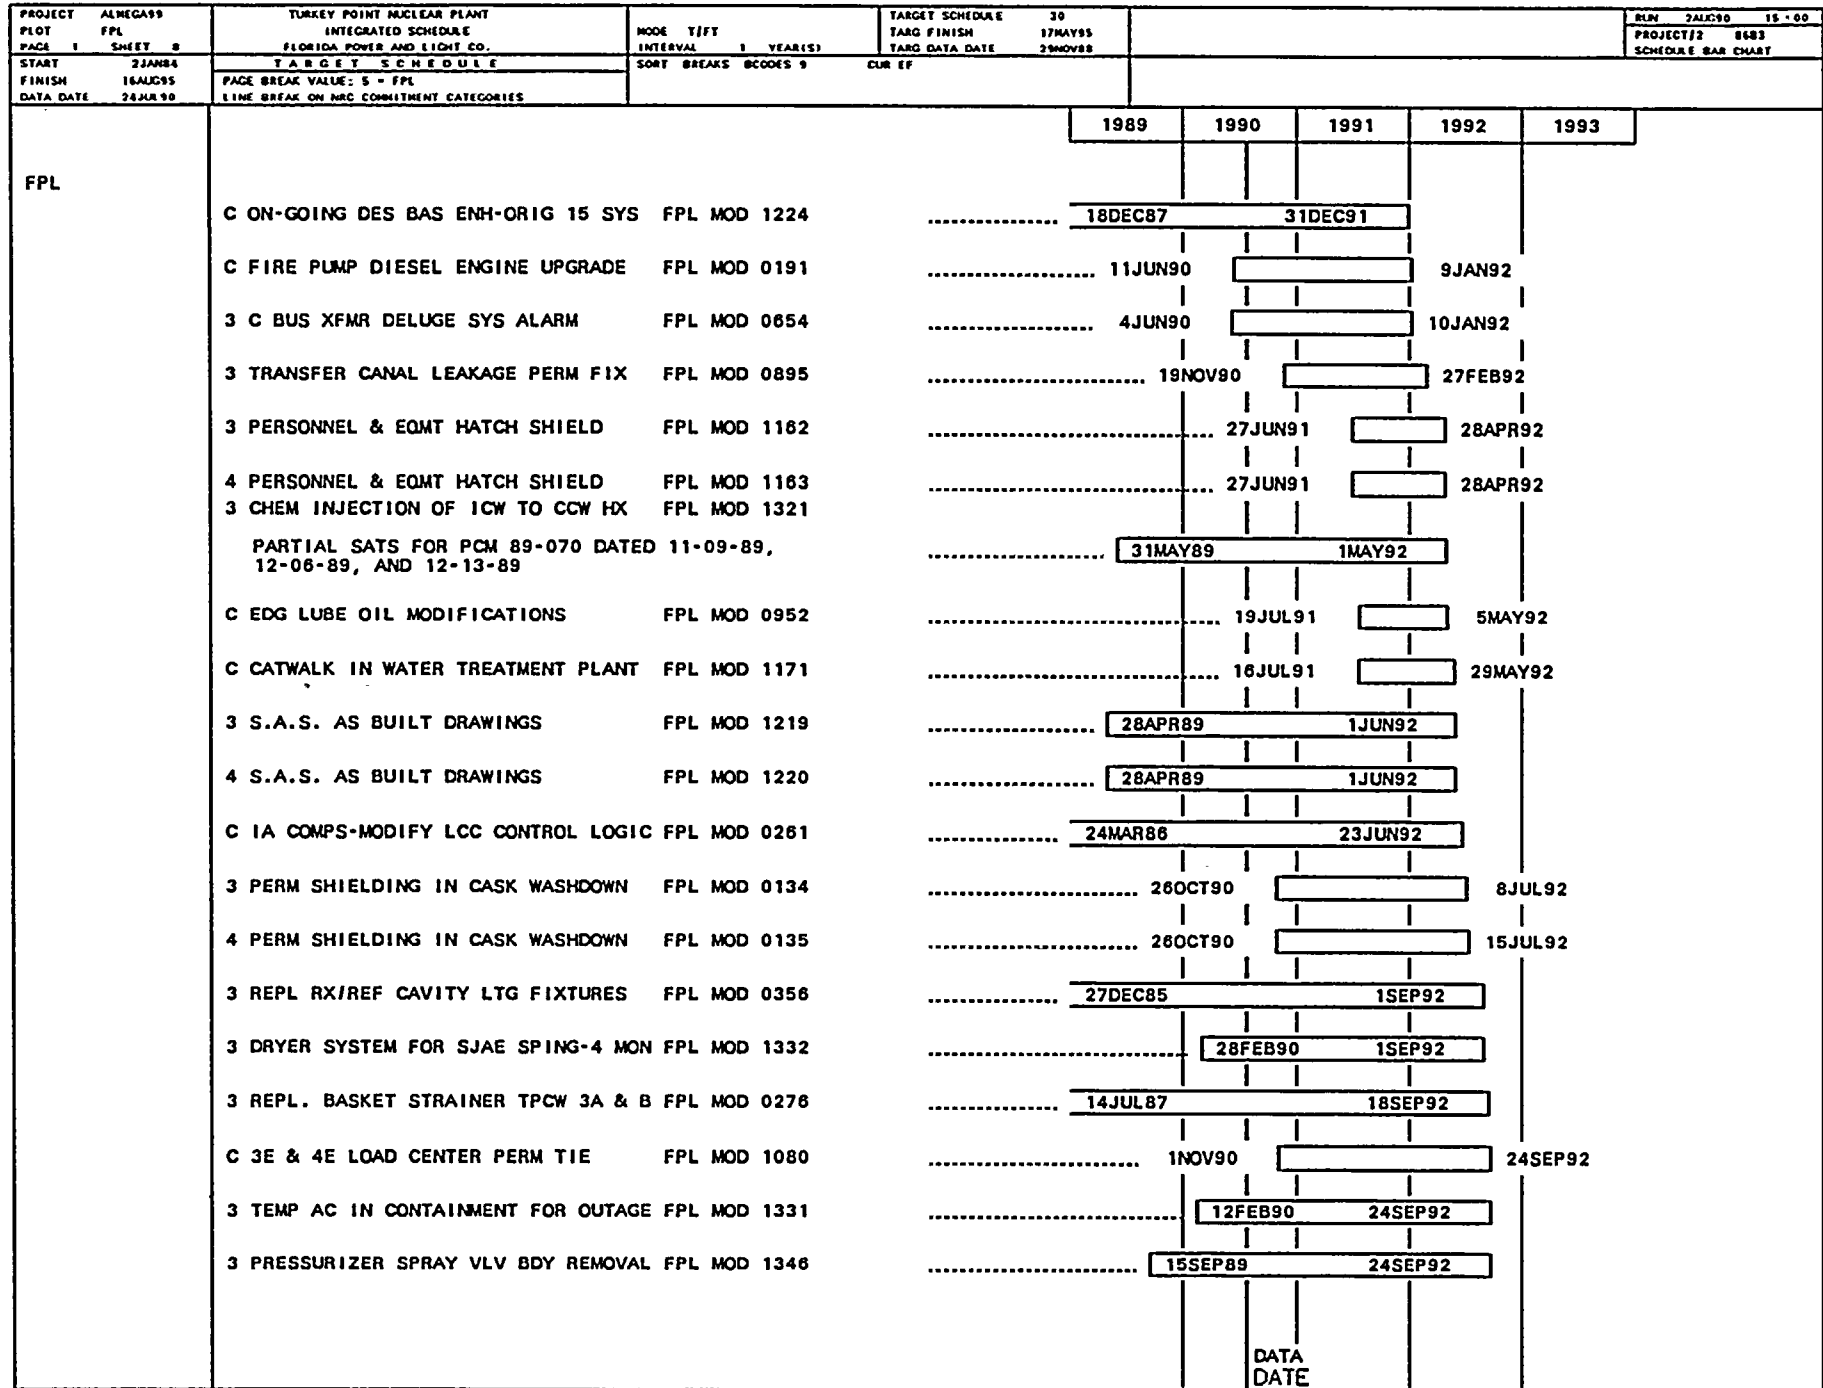

16.11.19



PROJECT ALMEGAS9	TURKEY POINT NUCLEAR PLANT	MODE T/J/F/T	TARGET SCHEDULE 30	ELN 2ALC90 15:00
PLOT FPL	INTEGRATED SCHEDULE	INTERVAL: 1 YEAR(S)	TARG FINISH 17MAY95	PROJECT# 8683
PAGE 1 SHEET 9	FLORIDA POWER AND LIGHT CO.		TARG DATA DATE 29NOV88	SCHEDULE BAR CHART
START 22JAN84	T A R G E T S C H E D U L E	SHORT BREAKS CODES 9	CUR EF	
FINISH 16AUG95	PAGE BREAK VALUE: 5 - FPL			
DATA DATE 24JUN 90	LINE BREAK ON NRC COMMITMENT CATEGORIES			

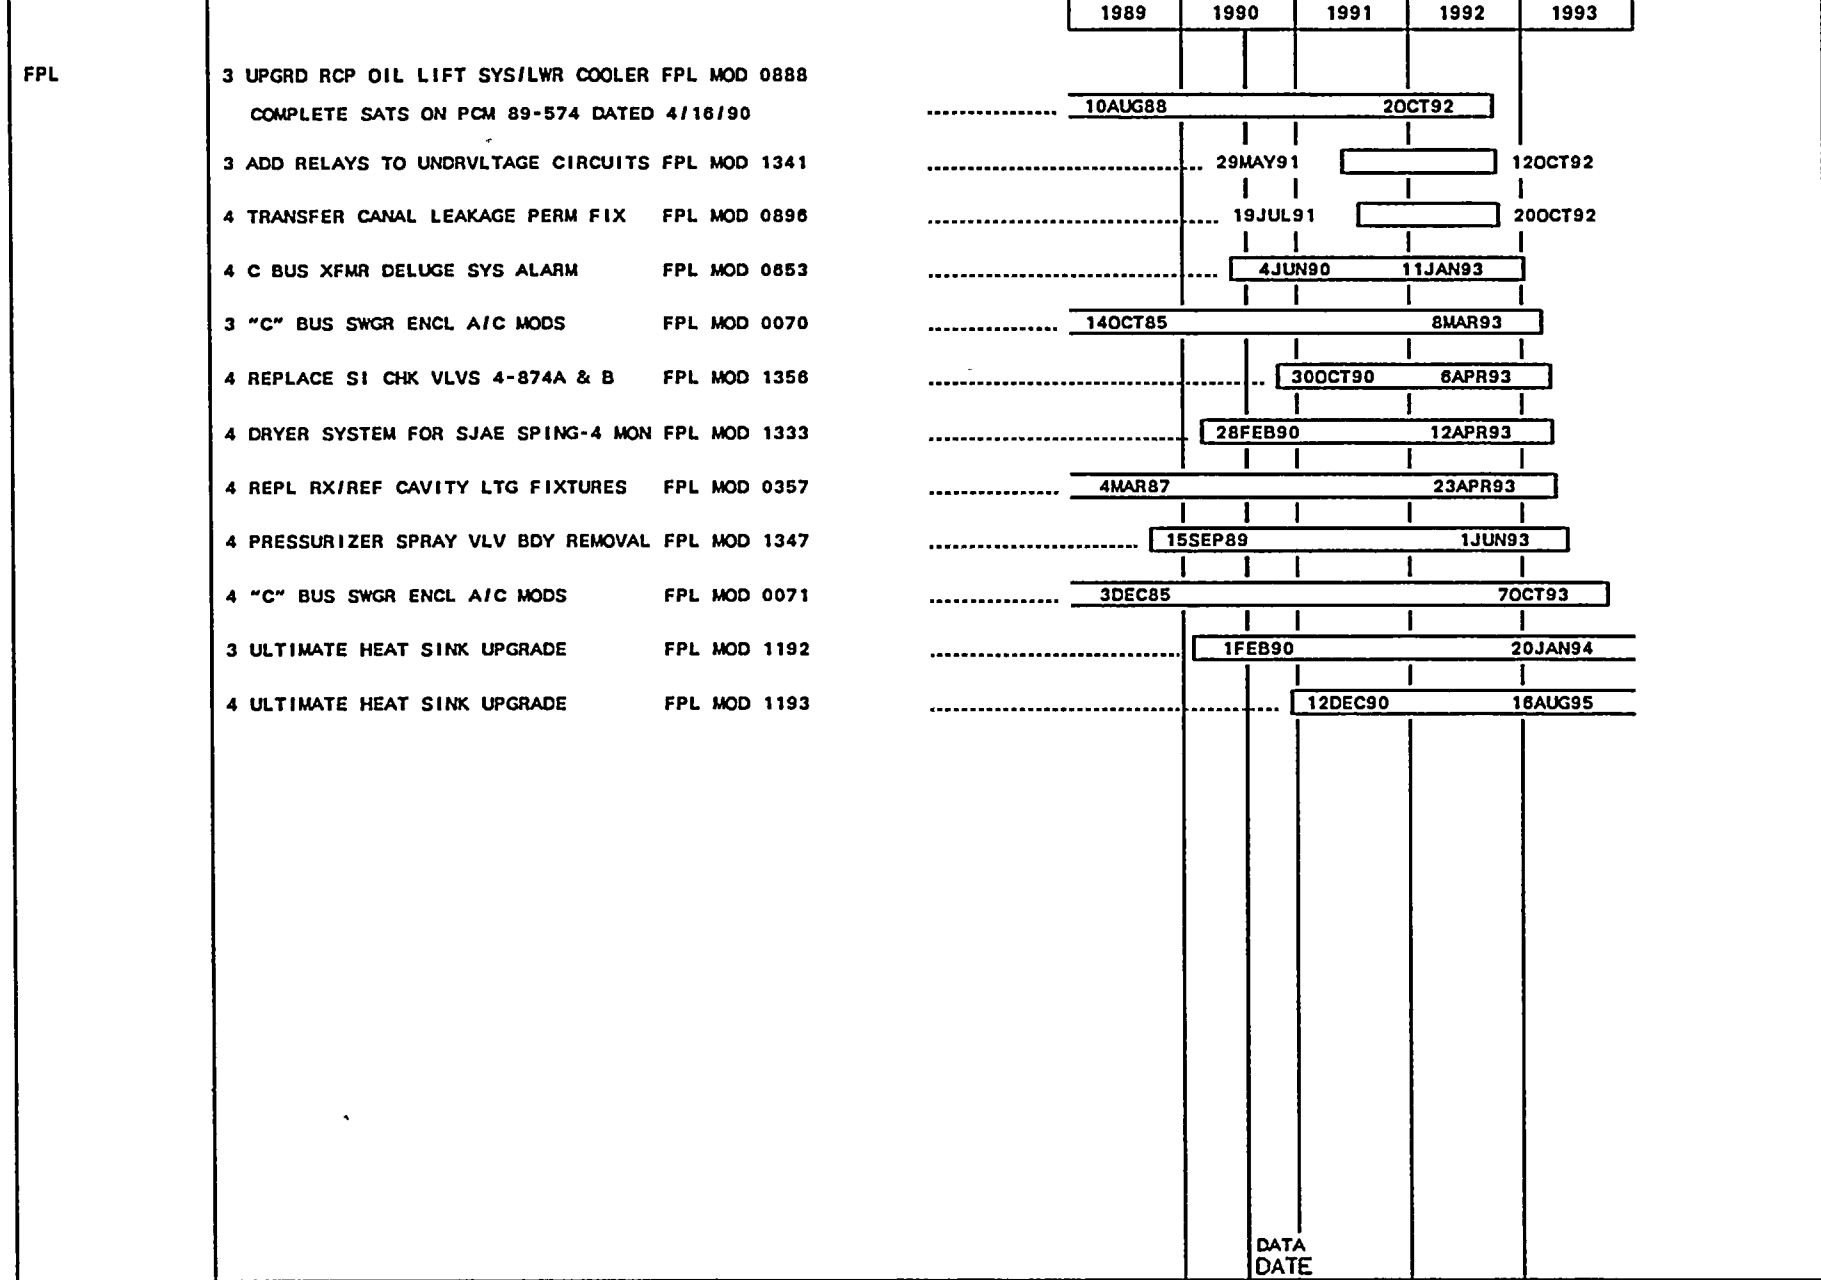

12  
1948
