

Vogtle

units 3&4 Nuclear Development



Vogtle 3&4 ITAAC Update


Mark Rauckhorst

Southern Nuclear Operating Company

July 7, 2015



ITAAC Closure Notification (ICN) Submittal – Units 3&4

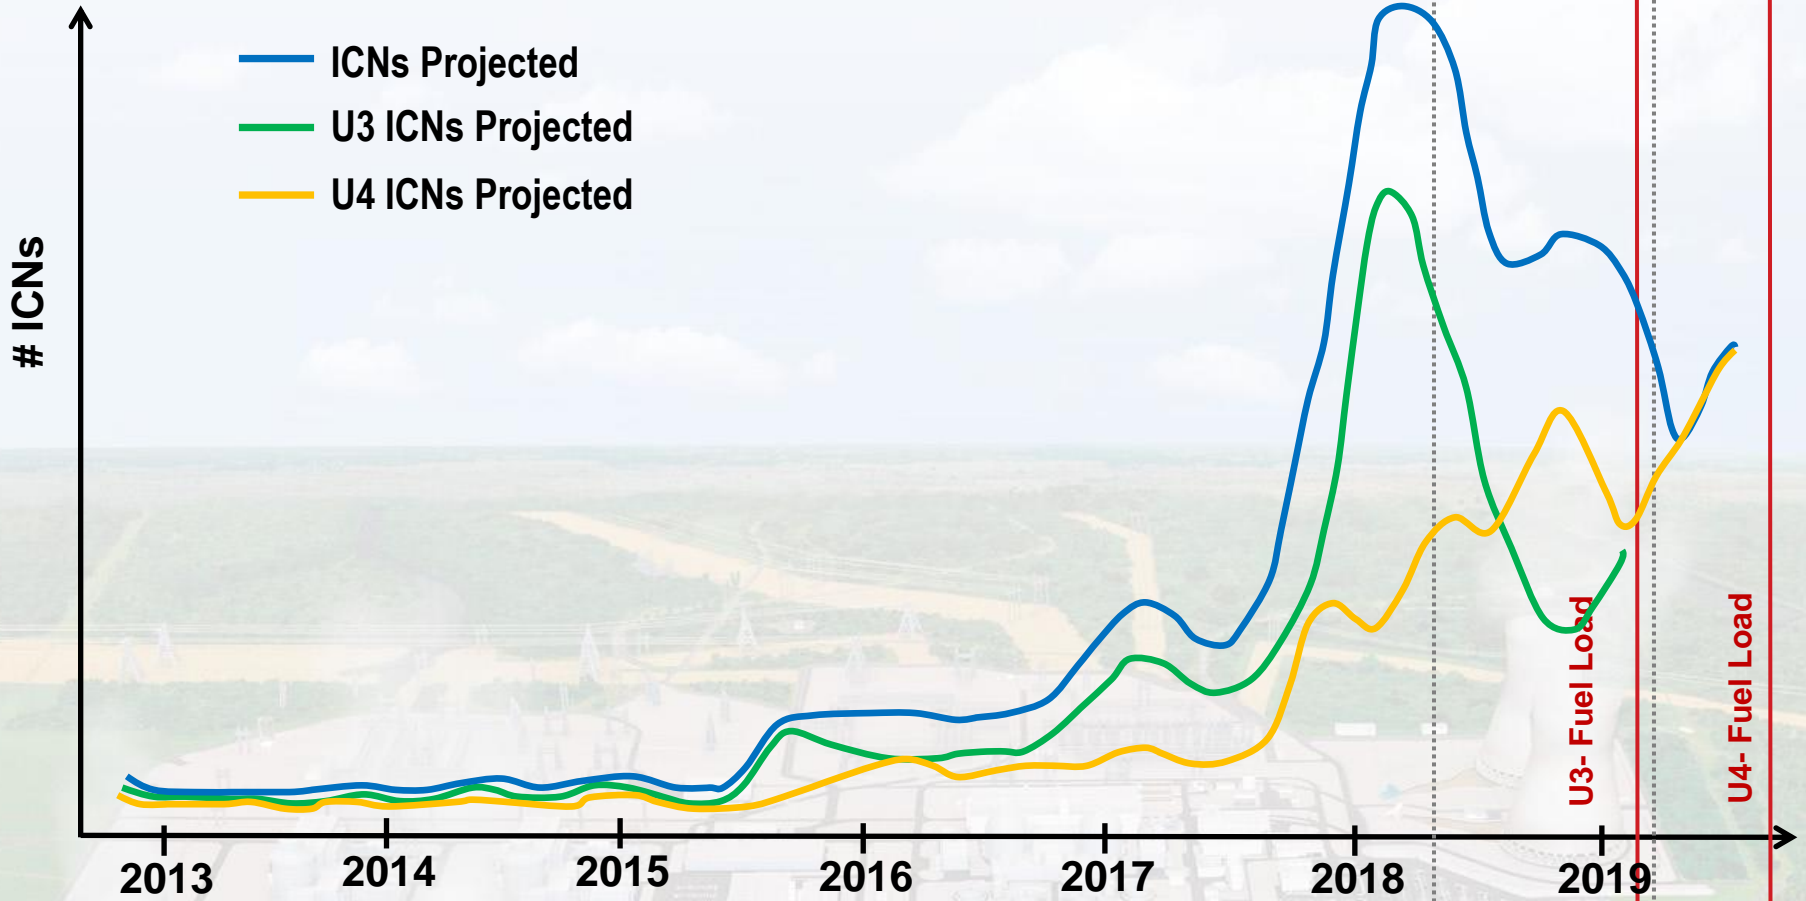

- ICNs Projected
- U3 ICNs Projected
- U4 ICNs Projected


U3 UIN

U4 UIN

U3- Fuel Load

U4- Fuel Load


ITAAC Life Cycle

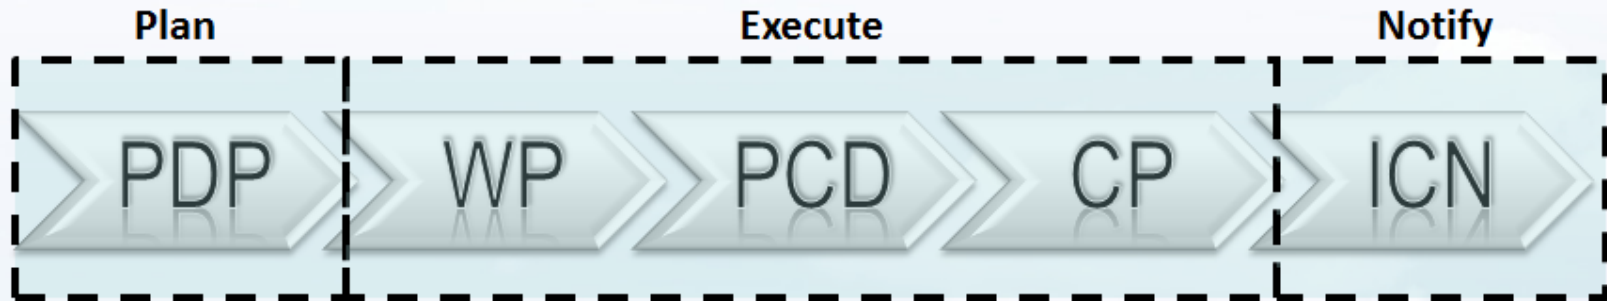

- **PDP** – Performance Documentation Plan
- **WP** – Work Package
- **PCD** – Principal Closure Document
- **CP** – Completion Package
- **ICN** – ITAAC Closure Notification

Life Cycle Status

Unit 3&4 Life Cycle Projection

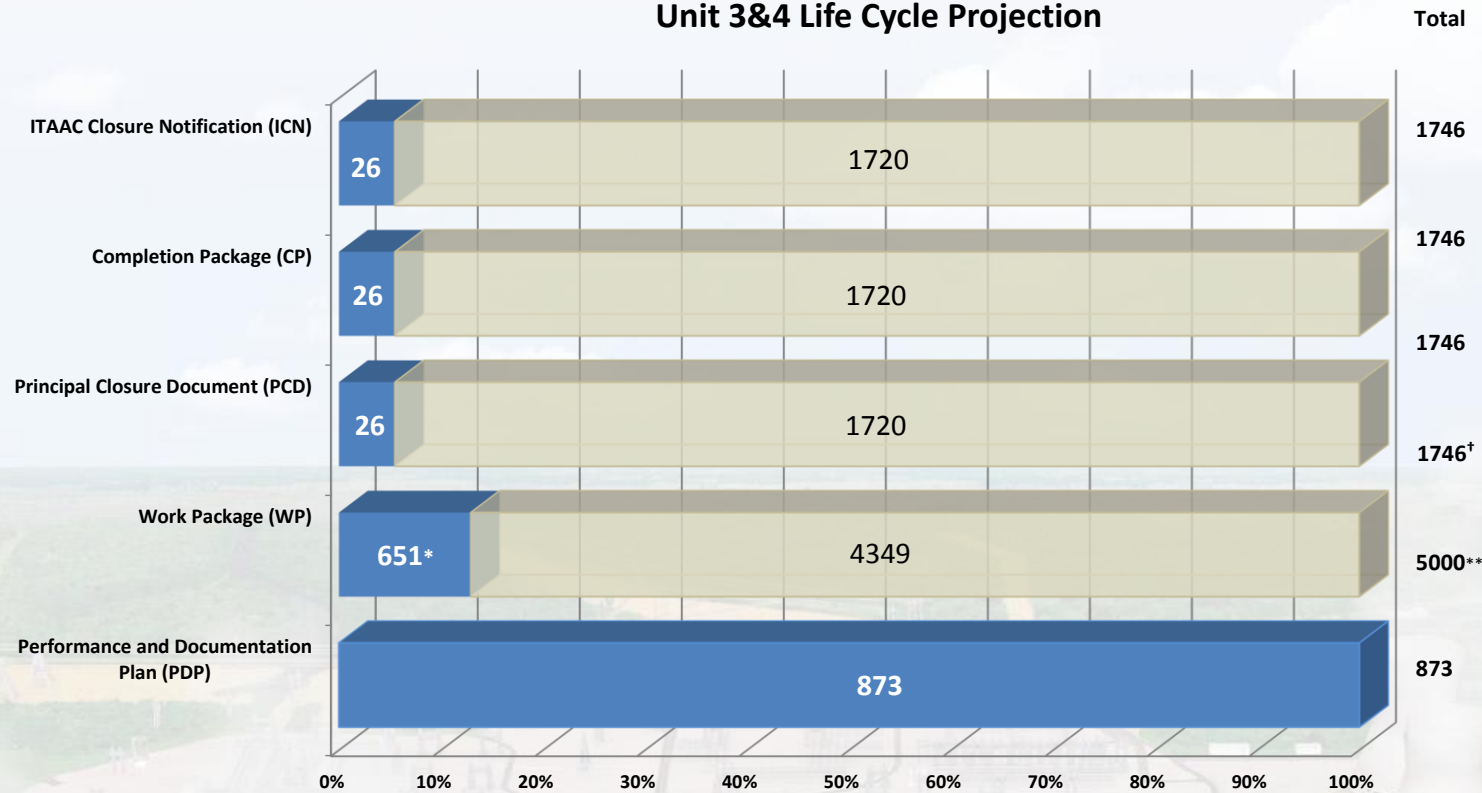

Note:

- [†]This number is under review to account for ITAAC with multiple PCDs.
- ^{*}WP screened as ITAAC applicable by CB&I Field Engineer prior to field implementation
- ^{**}Total project estimate of WP screened by CB&I as ITAAC applicable
- Projections reflect totals until the end of project with the exception of ICN 2015, which is yearly based.

■ Completed ■ Projected

Early Uncompleted ITAAC Notification (UIN) Submittal Update

- 10 CFR 52.99(c)(3), Licensee shall submit the UIN at least 225 days before fuel load
- Early UIN submittal path forward:
 - Construction Inspection Program Task Force
 - Evaluate current processes
 - Share results

Moving Forward

- Execution of ITAAC Maintenance
- Discuss opportunities related to early UIN submittal with NRC
- Utilize NRC inspection planning meetings to continue coordination with NRC

Vogtle
units 3&4



Nuclear Development



Vogtle
units 3&4 Nuclear Development

