MONITORING WELL COMPLETION LOG GRN01-0189

PROJECT UMTRA GROUND WATER
LOCATION GREEN RIVER, UT
SITE GREEN RIVER
WELL NUMBER 0189

NORTH COORD. (FT) 239061.15
EAST COORD. (FT) 2386726.24
HOLE DEPTH (FT) 20.00
WELL DEPTH (FT) 19.00

DATE DRILLED 06/05/2002
SURFACE ELEV. (FT NGVD) 4073.80
TOP OF CASING (FT) 4075.96
MEAS. PT. ELEV. (FT) 4075.96
SLOT SIZE (IN) 0.020
BIT SIZE(S) (IN) 8.0

WELL INSTALLATION		INTERVAL (FT)		
SURFACE CASING:				
BLANK CASING:	4 in. PVC Sch 40	-2.16	to	14.0
WELL SCREEN:	4 in. 0.02 Slotted PVC	14.0	to	19.0
SUMP/END CAP:				
SURFACE SEAL:				
GROUT:	Cement	0.0	to	2.0
SEAL:	Bentonite Pellets	2.0	to	11.0
UPPER PACK:	20-40 Silica Sand	11.0	to	12.0
LOWER PACK:	10-20 Silica Sand	12.0	to	19.0

DRILLING METHOD ROTASONIC
SAMPLING METHOD ROTASONIC CORE
DATE DEVELOPED
WATER LEVEL (FT BGS) Dry 06/05/2002
LOGGED BY Dayvault, R.
REMARKS

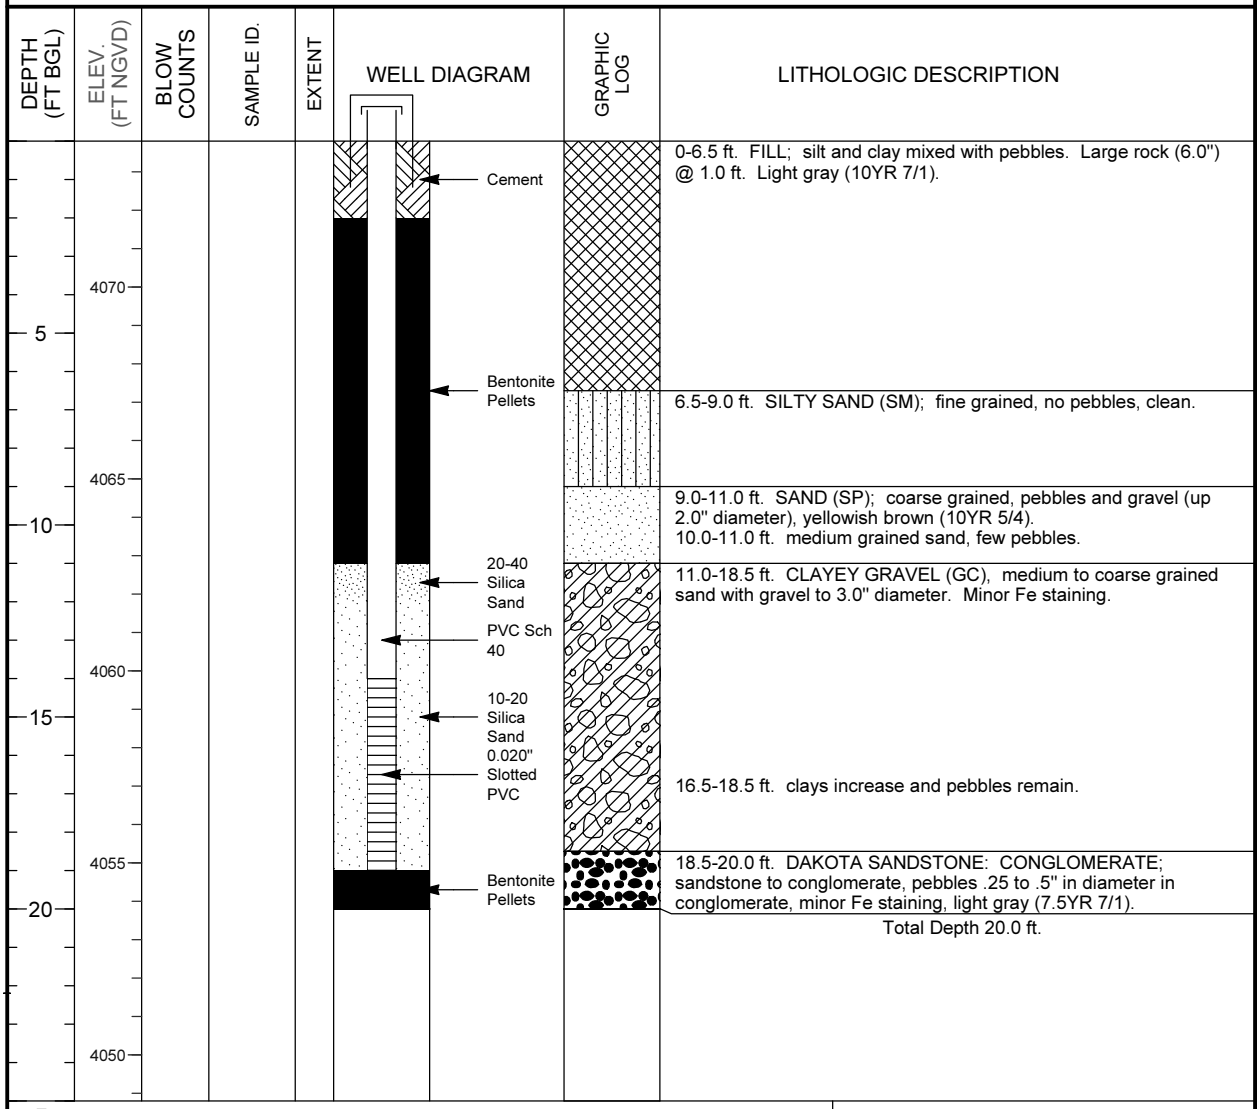

Stoller–GJO

U.S. DEPARTMENT OF ENERGY
GRAND JUNCTION OFFICE, COLORADO
